

THE CITY OF NEW YORK  
DEPARTMENT OF ENVIRONMENTAL PROTECTION  
BUREAU OF WATER POLLUTION CONTROL

BOROUGH OF S.I.

CERTIFICATE OF INSPECTION  
NEW SEWER HOUSE CONNECTION

The following described sewer house connection has been laid from the property line to the existing sewer at premises:

N.B.# 754/78 BLOCK 2073 LOT 37  
UNDER PERMIT NO. 4333 ISSUED 2-29-80  
PREMISES 47 Saybrook St.  
(HOUSE NUMBER AND STREET)  
LOCATED EAST SIDE, FEET SOUTH OF VICTORY BLVD.  
OWNER HOWEY BEE HOMES INC.  
PLUMBER THUTZER PLUMBING  
SIZE AND TYPE OF PIPE LAID 6" CAST IRON  
CONN. TO (SIZE, TYPE) 10" ESUP SEWER LOCATED IN  
(STREET/AVENUE) SAYBROOK ST.

I HEREBY CERTIFY THAT I MADE THE INSPECTION OF THE SEWER HOUSE CONNECTION DESCRIBED ABOVE AND THAT ALL WORK DONE UNDER THIS PERMIT HAS BEEN PROPERLY COMPLETED IN ACCORDANCE WITH EXISTING ORDINANCES AND RULES AND REGULATIONS.

DATE: 10/19/78 NAME (PRINT) RICHARD CRESANIS  
SIGNED Richard Cresanis  
INSPECTOR-DIVISION OF SEWER CONSTRUCTION  
NOTED \_\_\_\_\_  
BOROUGH ENGINEER

PENALTY FOR FALSIFICATION:  
FALSIFICATION OF ANY STATEMENT MADE HEREIN IS AN OFFENSE PUNISHABLE BY A FINE OR IMPRISONMENT OR BOTH (N.Y.C. ADMINISTRATIVE CODE, SECTION 1151-9.0)

Copies to:      Borough Superintendent, Department of Buildings  
     Borough Office, Bureau of Water Engineer  
     Sewer Regulation and Control Section  
File original in Borough Construction Office

NOTE: The sewer to which the house connection is made is       
is not      connected to a private sewer treatment plant.  
Form No. WPC-15 Rev. B (6-77) (Yellow)


47	Saybrook St.	2073	37
HOUSE NUMBER	STREET NAME	BLOCK	LOT

1. Was connection extended from existing curb connection?  YES /  NO
2. Was the connection placed on (earth) stone or crushed rock, concrete cradle, concrete encasement, or reinforced concrete encasement? (Circle)
3. Was connection made to existing spur or riser or cut in? (Circle)
4. If connection was "cut in", was saddle or dutchman used? (Circle, if yes)

5. Length, size and material of new connection 20' - 6" Cast Iron

6. Depth of connection at curb line is 9' feet.

7. All work was exposed and inspected.

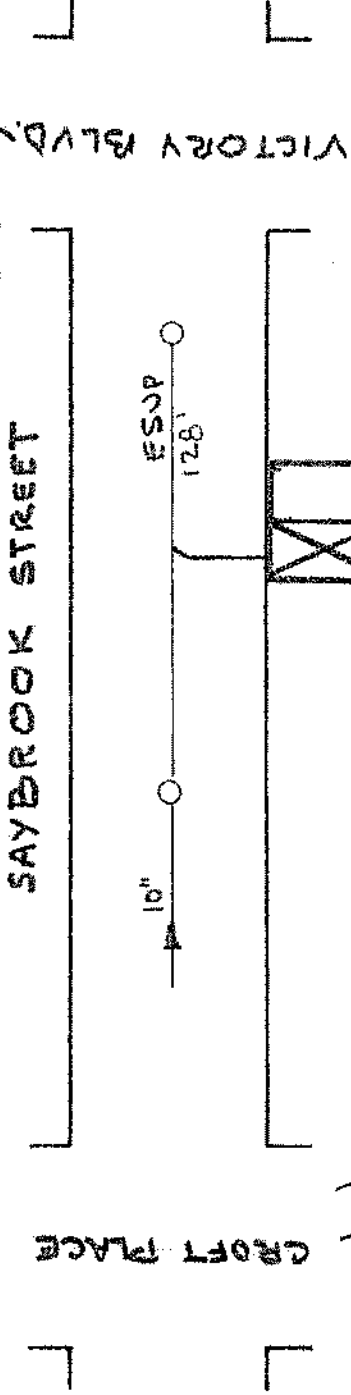

DATE: 10/19/78

SIGNED

INSPECTOR-DIVISION OF SEWER CONSTRUCTION
