

THE CITY OF NEW YORK  
DEPARTMENT OF ENVIRONMENTAL PROTECTION  
BUREAU OF WATER POLLUTION CONTROL

BOROUGH OF RICHMOND

CERTIFICATE OF INSPECTION

NEW SEWER HOUSE CONNECTION

The following described sewer house connection has been laid from the property line to the existing sewer at premises:

N.B.# 20/78 BLOCK 2674 LOT 37

UNDER PERMIT NO. 4266 ISSUED 3-25-78

PREMISES 33 GOLLER PLACE S.I.  
(HOUSE NUMBER AND STREET)

LOCATED EAST SIDE, 29402 FEET South OF VICTORY

OWNER GOLLER PLACE CO-OP.

PLUMBER BROOK WATTEN-JBL

SIZE AND TYPE OF PIPE LAID 10" CAST IRON

CONN. TO (SIZE, TYPE) 10" ESVP SAND SEWER LOCATED IN

(STREET/AVENUE) GOLLER PLACE

I HEREBY CERTIFY THAT I MADE THE INSPECTION OF THE SEWER HOUSE CONNECTION DESCRIBED ABOVE AND THAT ALL WORK DONE UNDER THIS PERMIT HAS BEEN PROPERLY COMPLETED IN ACCORDANCE WITH EXISTING ORDINANCES AND RULES AND REGULATIONS.

DATE: JULY 19, 1978 NAME (PRINT) BROCK SUCHER

SIGNED Brock Sucher  
INSPECTOR-DIVISION OF SEWER CONSTRUCTION

NOTED \_\_\_\_\_  
BOROUGH ENGINEER

PENALTY FOR FALSIFICATION:  
FALSIFICATION OF ANY STATEMENT MADE HEREIN IS AN OFFENSE PUNISHABLE BY A FINE OR IMPRISONMENT OR BOTH (N.Y.C. ADMINISTRATIVE CODE, SECTION 1151-9.0)

Copies to: \_\_\_\_\_ Borough Superintendent, Department of Buildings  
\_\_\_\_\_ Borough Office, Bureau of Water Register  
\_\_\_\_\_ Sewer Regulation and Control Section  
File original in Borough Construction Office

NOTE: The sewer to which the house connection is made is  is not  connected to a private sewer treatment plant.  
Form No. WPC-15 Rev. B (6-77) [Yellow]


HOUSE NUMBER <u>33</u>	STREET NAME <u>Colter Place</u>	BLOCK <u>2074</u>	LOT <u>37</u>
---------------------------	------------------------------------	----------------------	------------------

1. Was connection extended from existing curb connection?  YES  NO
2. Was the connection placed on earth, stone or crushed rock, concrete cradle, concrete encasement, or reinforced concrete encasement? (Circle)
3. Was connection made to existing spur or riser or cut in? (Circle)
4. If connection was "cut in", was saddle or dutchman used? (Circle, if yes)

5. Length, size and material of new connection 25' 6" Cast Iron

6. Depth of connection at curb line is 6 1/2 feet.

7. All work was exposed and inspected.

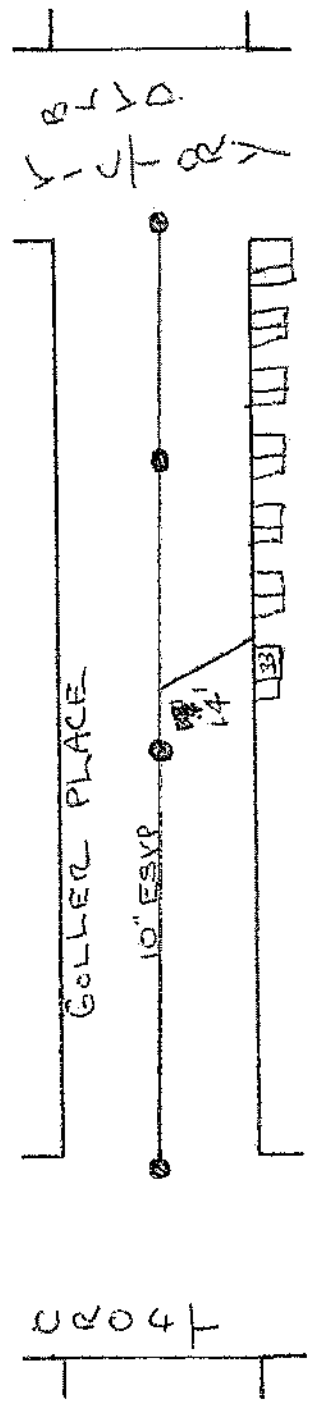

DATE: July 20, 1978 SIGNED \_\_\_\_\_ INSPECTOR-DIVISION OF SEWER CONSTRUCTION
