


ALTERNATE DRIP EDGE CLEAT

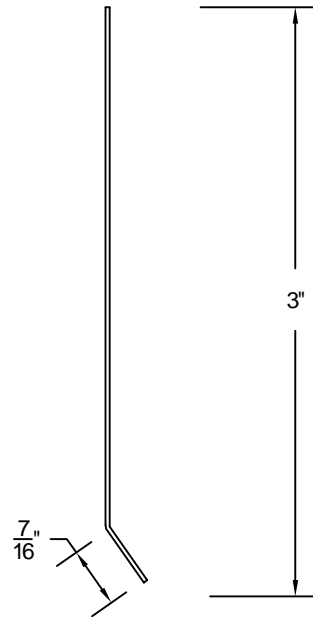

MATERIAL (please choose one):

- 22 GA Steel
 20 GA Steel

OTHER
(PARTS ARE MILL FINISH)

OTHER: _____

Quantities:

_____ Total Linear Feet (10'-0" Lengths)

Miter/End Cap additional information:

See the attached sheets for miters and end cap

Installation:

- 1) Fastened at 6" O/C minimum or otherwise noted.
- 2) 1.5" SS Ring Shank nails, minimum
- 3) Splice plates require 2 beads of sealant per side at splice

Sheet ___ of ___.

DWG# 730-009

Notes:

- 1) Written approval is required prior to fabrication, contractor is responsible for all dimensions and quantities. Fabricated items are not returnable.
- 2) Parts are mill finish unless otherwise indicated

Temple Architectural Products
638 Moore Rd
Avon Lake, OH 44012

Phone: (216) 440-3595
Alternate: (330) 348-3983
Fax: (440) 653-9883

Project Name: _____

Installing Contractor: _____

Contact Name: _____

Contact number: _____

Signed Approval: _____
