

PEAK & VALLEY MITERS



TEMPLE
Architectural Products

PEAK MITER FRONT VIEW

☐ TAPERED COPING

☐ FLAT COPING

WALL SIZE _____

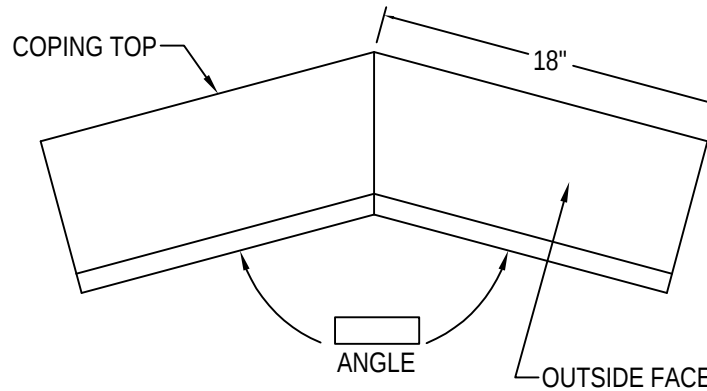



ANSI/SPRI ES-1*

VALLEY MITER FRONT VIEW

☐ TAPERED COPING

☐ FLAT COPING

WALL SIZE _____

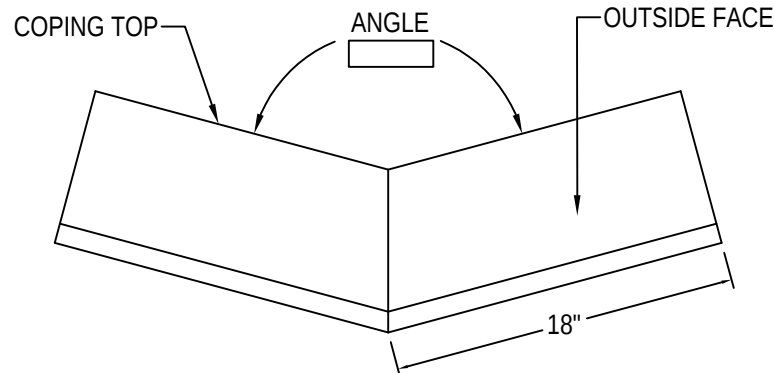

MATERIAL (please choose one):

☐ 24 GA Steel

☐ 22 GA Steel

☐ .032 Aluminum

☐ .040 Aluminum

☐ .050 Aluminum

☐ .063 Aluminum

Other: _____

Color: _____

Finish: _____

Quantities:

_____ PEAK MITER (S)

_____ VALLEY MITER (S)

Miter/End Cap Fabrication Requirements:

☐ Pop Rivet & Sealed

☐ Welded (see note)*

Installation:

1) Cleats are to be installed 40" O/C, coping hem crimped to cleat

2) 8 - 1.5" SS Ring Shank nails per cleat, minimum

3) Splice plates require 2 beads of sealant per side of coping

Sheet ____ of ____.

DWG# 740-021

Notes:

- 1) *Accessory Welding is only available in 050 aluminum or heavier
- 2) External splice plates are available upon request
- 3) Written approval is required prior to fabrication, contractor is responsible for all dimensions and quantities. Fabricated items are not returnable.

Temple Architectural Products
1111 Lowell St.
Elyria, OH 44035

Phone: (440) 323-9393

Fax: (440) 412-7559

Project Name: _____

Installing Contractor: _____

Contact Name: _____

Contact number: _____

Signed Approval: _____
