


# STANDARD GRAVEL STOP CLEAT

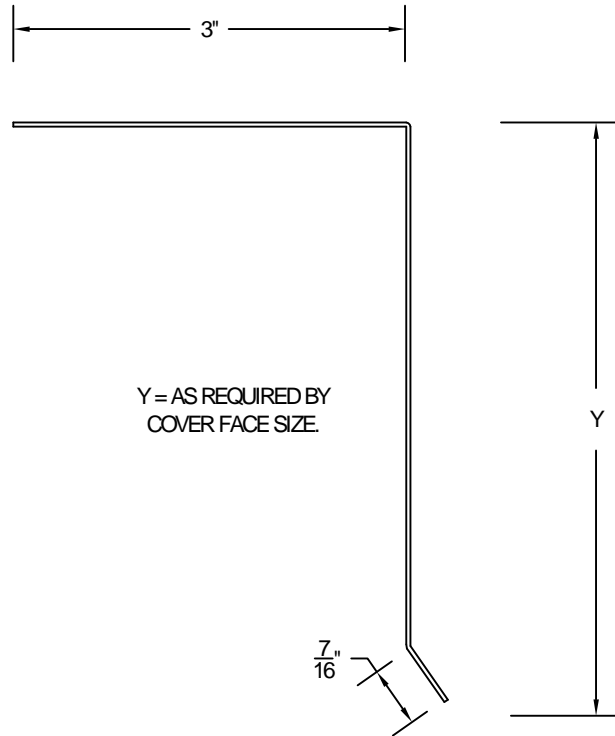

MATERIAL (please choose one):

- |                                      |                                |
|--------------------------------------|--------------------------------|
| <input type="checkbox"/> 22 GA Steel | <input type="checkbox"/> OTHER |
| <input type="checkbox"/> 20 GA Steel | (PARTS ARE MILL FINISH)        |

OTHER: \_\_\_\_\_

Quantities:

\_\_\_\_\_ Total Linear Feet (10'-0" Lengths)

Miter/End Cap additional information:

See the attached sheets for miters and end cap

Installation:

- 1) Fastened at 6" O/C minimum or otherwise noted.
- 2) 1.5" SS Ring Shank nails, minimum
- 3) Splice plates require 2 beads of sealant per side at splice

Sheet \_\_\_ of \_\_\_.

DWG# 730-008

**Notes:**

- 1) Written approval is required prior to fabrication, contractor is responsible for all dimensions and quantities. Fabricated items are not returnable.
- 2) Parts are mill finish unless otherwise indicated

Temple Architectural Products  
638 Moore Rd  
Avon Lake, OH 44012

Phone: (216) 440-3595  
Alternate: (330) 348-3983  
Fax: (440) 653-9883

Project Name: \_\_\_\_\_

Installing Contractor: \_\_\_\_\_

Contact Name: \_\_\_\_\_

Contact number: \_\_\_\_\_

Signed Approval: \_\_\_\_\_
