

GP CPCS  
Report:  
September 2021

10<sup>th</sup> October 2021



**Greater Manchester  
Community Pharmacy**  
Provider Board

# September Update

## Governance

- EMIS procurement saw a temporary solution in September:
  - a 3-month SLA was agreed, with a waiver signed by SRFT to allow this
  - 128 named practices (taken from the deployment plan in mid-August) were included in the 3-month agreement
  - Pinnacle / EMIS and GMSS have agreed that changes can be made to the named practices included in the SLA as long as the net cost remains under the amount agreed in the waiver
  - Final SBS contract with EMIS (who are on the procurement framework) with call-off will be ready before the end of November
- Fortnightly meetings with LB as SRO, GMHSCP finance & GMSS continue
- An issue was highlighted where a number of practices had completed deployment but not subsequently made an referrals – an escalation process was proposed, and a GP commitment created and introduced into the deployment plan to mitigate. Further work in October to progress this ownership & accountability work with general practice colleagues through PCB and GPPB
- Working group ToR updated and finalised
- Release of IIF detail re incentives for general practice – further work needed to understand and build into the deployment plan
- PCN engagement spend reviewed and agreed in Wg meeting

## Engagement

- GM association of LMCs flagged as an engagement gap – further liaison to arrange a meeting in October
- GPPB update slot pushed into October due to full agenda
- Further discussions with Wigan locality with several meetings attended to engage
- Agreement around timing of engaging new practices re Christmas and 3-month SLA for IT referral mechanism – tricky balance to find – agreed to step down any practices who are not responsive and make contact again in January; focus attention on responsive practices only to get them live before Christmas
- Offer from RPS of training for CPCS with GM introduction was received and accepted – further work

## Project Planning

- Feedback received around suitability of the GM Referral protocol following 2 examples in 1 GM locality. It was discussed whether a local review of this nationally prepared document was appropriate with key stakeholders in GM. Decision was taken that this review should be on hold pending on further feedback locally and in discussion with NHSE&I if required
- Deployment plan and blueprint – working group reflected on experience of following both and identified some opportunities to streamline, to automate and to include learnings from 6 months of deployment. Plan was updated and blueprint to be reviewed in October. Mail merge was adopted for several steps in the process which could be optimised and some steps were removed. Additional look ups were added to show any pharmacy issues
- A review of NHS 111 CPCS referral activity was conducted to inform the pharmacy deployment plan and highlight best practice, as well as any issues with responsiveness
- Pharmacy mapping activities were conducted in September to map all practices in the deployment plan
- Provision of training to practice staff was reviewed and optimised – 2 sessions per week at the times and days most often requested by general practice have been set up and made available for practices to book onto directly via Eventbrite
- Update on translation services confirmed that the funding currently sits with CCGs and 1 CCG approached is open to community pharmacy accessing existing services for GP CPCS consultations. Further work in October to discuss more widely
- Cross-border pharmacies and GPs mapped and detail and proposed process discussed & agreed with NW colleagues
- Process regarding email verification of practices with PharmOutcomes to receive notifications clarified with Pinnacle
- Request submitted to Pinnacle for a referral rejection to be sent electronically to the practice – currently this functionality is not in place. KN confirmed this is being looked into.

## Deployment

- 44 practices went live in September
- Total 77 practices live, 42 actively referring
- PharmOutcomes / Outcomes for Health log in set up for EMIS practices required to access data and reports at practice level – need to revisit details in deployment cohorts sent to EMIS and update information – further work in October

Deployment update


# Deployment Overview

Status Date: 11/10/2021

Number of General Practices in Deployment  
by Deployment Status

Deployment Stage	Number of Practices	% of GM practices
1 Initial Engagement	99	23%
2 Pre Implementation	29	7%
3 Implementation	29	7%
4 Go Live	12	3%
5 Post Go Live	46	11%
6 Implementation complete	31	7%

**246 (56%) of GM General Practices are currently in deployment**

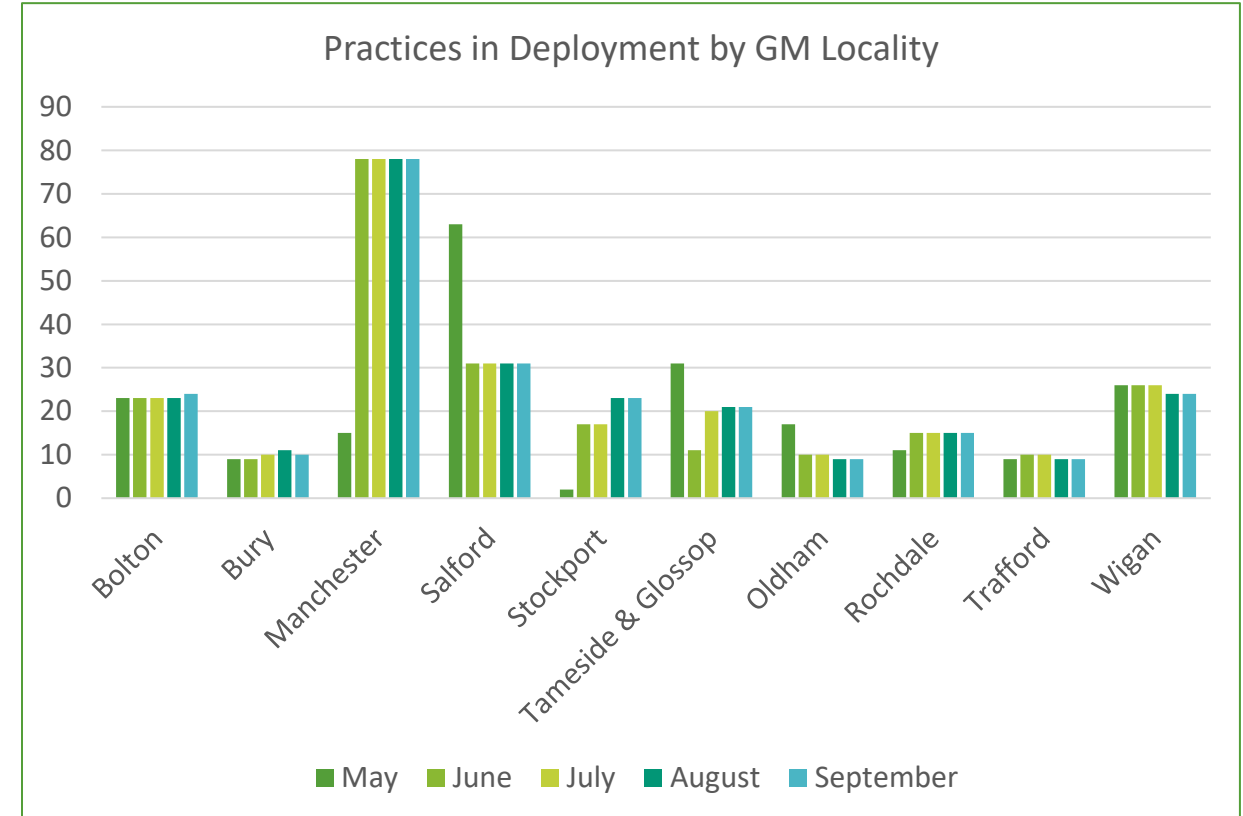

Targeted engagement work ongoing in several GM localities to address inequities.

MHCC have provided resource to support the deployment in Manchester over and above the working group resource provided.

# Deployment Overview by GM Locality

	Number of Practices	% Practices at Initial Engagement	% Practices at Pre-Implementation	% Practices at Implementation (training)	% Practices at Go Live	% Practices Post Go Live (within 4 weeks of go live date)	% Practices Deployment Completed (>4 weeks post go live)
Bolton	49	2%	20%	4%	4%	24%	2%
Bury	26	15%	19%	0%	0%	0%	8%
HMR	36	17%	0%	0%	0%	0%	25%
Manchester	85	0%	11%	26%	7%	29%	19%
Oldham	39	3%	10%	3%	0%	8%	0%
Salford	38	34%	0%	0%	0%	0%	0%
Stockport	36	36%	8%	0%	11%	8%	0%
T&G	37	35%	3%	11%	0%	8%	0%
Trafford	27	22%	0%	0%	0%	0%	11%
Wigan	58	41%	0%	0%	0%	0%	0%

# Deployment Activity

Deployment Stage	Number of meetings held	Number of General Practices represented
1 Initial Engagement	3	4
2 Pre Implementation	6	6
3 Implementation	4	10

## Deployment Resource:

LPC resource is provided from core LPC funding (contractual levy from pharmacy contractors) – no additional funding has been received to deploy GP CPCS. CHL resource for 6 months agreed from minimal existing project funds held.

## Deployment Resource in July:

Bolton LPC: 34 hours (n=1)

CHL hours: 65 hours (n=2)


GMLPC: 91 hours (n=4)

## Deployment update:

September was a very active month for practices going live, as the IT referral mechanism situation was temporarily resolved.

The focus for the working group was to support as many practices to go live as possible, who had been trained over the summer and were awaiting resolution of the IT referral mechanism.

## Live practices by Locality



**Practices Live : 77 (42 active)**  
**Total Referrals to end Sep: 1679**

# GP CPCS Objectives: Key

Objectives 1 & 2	
	On track or achieved
	Requires improvement
	Significant issues
	Not applicable

Objective #3	
Within the calendar month:	
>=75% of live practices met referral target	
>=75% of live practices made some referrals	
>25% of live practices did not make any referrals	

Objective #4	
Within the calendar month:	
>70% referrals completed within 12 hours	
60-69% referrals completed within 12 hours	
<60% referrals completed within 12 hours	

# GP CPCS Objectives: September

Objectives	May-21	Jun-21	Jul-21	Aug-21	Sep-21
<b>50% Practices live by 31/03/2022</b>	0.20%	0.20%	0.20%	0.20%	20.37%
<b>75% Practices live by 31/03/2023</b>	N/A	N/A	N/A	N/A	N/A
<b>Target number of referrals per week for live practices*</b>	67%	75%	90%	89%	54%
<b>70% referrals completed within 12 hours</b>	96.40%	93.40%	95%	92%	84%

\*36 practices have gone through deployment but not made any referrals

29 practices have made some referrals

13 practices have referred to the targets agreed (3% of appointments based on practice list size)




# Deployment Success Criteria: September


Success Criteria	May-21	Jun-21	Jul-21	Aug-21	Sep-21
GM Processes defined, documented & signed off ready for adoption in deployment					
100% of EMIS General Practices included in the deployment plan have the EMIS CPCS template installed & ready for use by agreed date					100%
100% of non-EMIS General Practices included in the deployment plan have access to PharmRefer by agreed date					100%
80% of identified general practice staff have completed GP CPCS training before go live date					83%
95% of pharmacies identified as likely to receive referrals from a general practice included in the deployment plan have been informed & confirmed readiness	87%		100%		100%
80% of general practices included in the deployment plan make a referral in the week they go live	67%		100%		70%
70% of referrals completed by community pharmacy within timeframes specified in the service specification and toolkit – within 12 hours or the next working day.	96%	93%	95%	92%	84%

# Activity report

# Referral Activity Trend

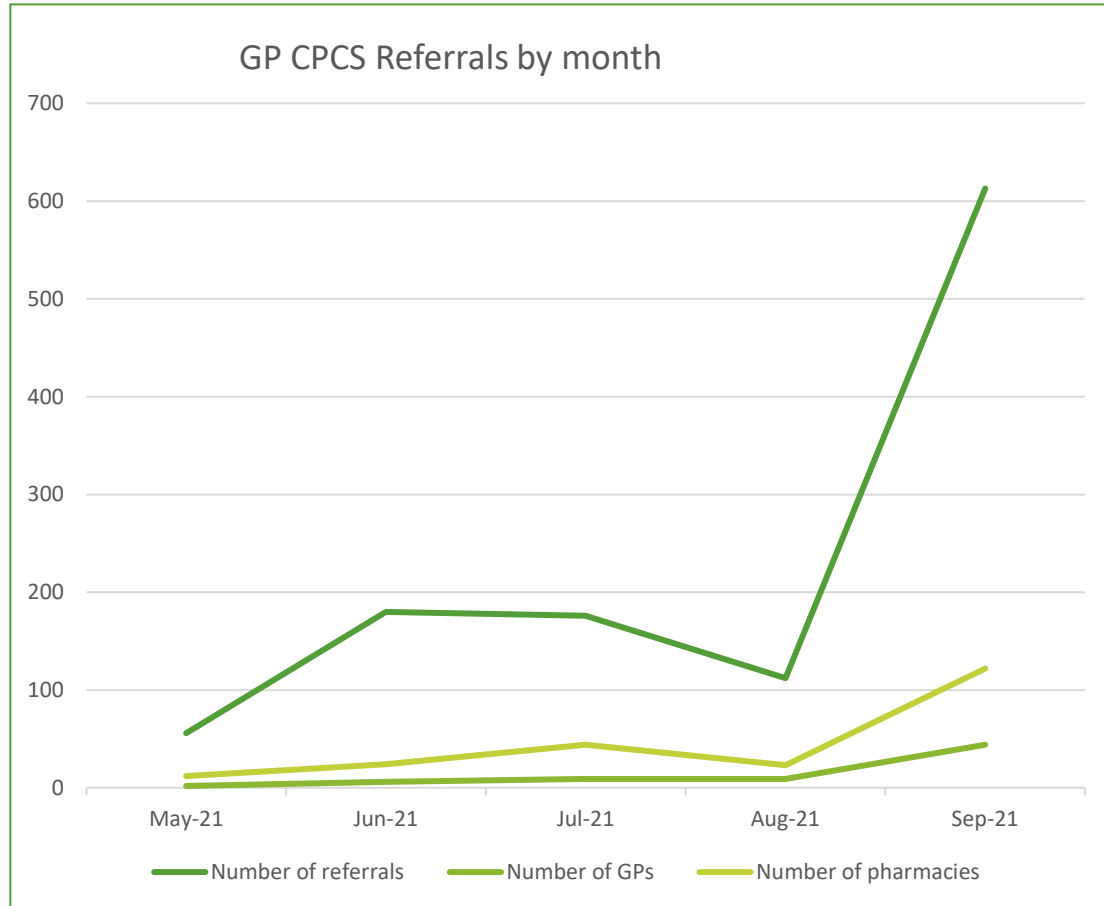

There was a significant increase in referral activity in September resulting from 44 practices going live in the month



# September Referral Activity

## Consultation Outcomes:

Number of Referrals sent	Number of General Practices actively referring	Number of Pharmacies referred to
613	42	122

Advice only  
186

Advice & OTC sale  
89

Advice & MAS supply  
35

Advice & non-urgent referral  
88

Urgent Escalation  
44

Urgent Escalation (A&E)  
3

### Escalations

Of **88 Non-urgent escalations**, 80 were to GP and 8 to other healthcare professionals (14% referrals).


In the pilot, it was observed that there was a greater number of non-urgent escalations in the early days of the referral pathway commencing, whilst the practice staff got used to identifying appropriate patients to refer.

It is anticipated this should average out at around 10-12% once the service is embedded.


Of **44 urgent escalations**, all were a same-day appointment request to GP.

Of **3 urgent escalations**, 2 patients were referred to A&E, one with numbness in the legs and back, and one with shortness of breath. The 3<sup>rd</sup> patient was escalated to the urgent NHS 111 clinical hub with a very bad cough lasting over 3 weeks


# Number of practices at each deployment stage by locality

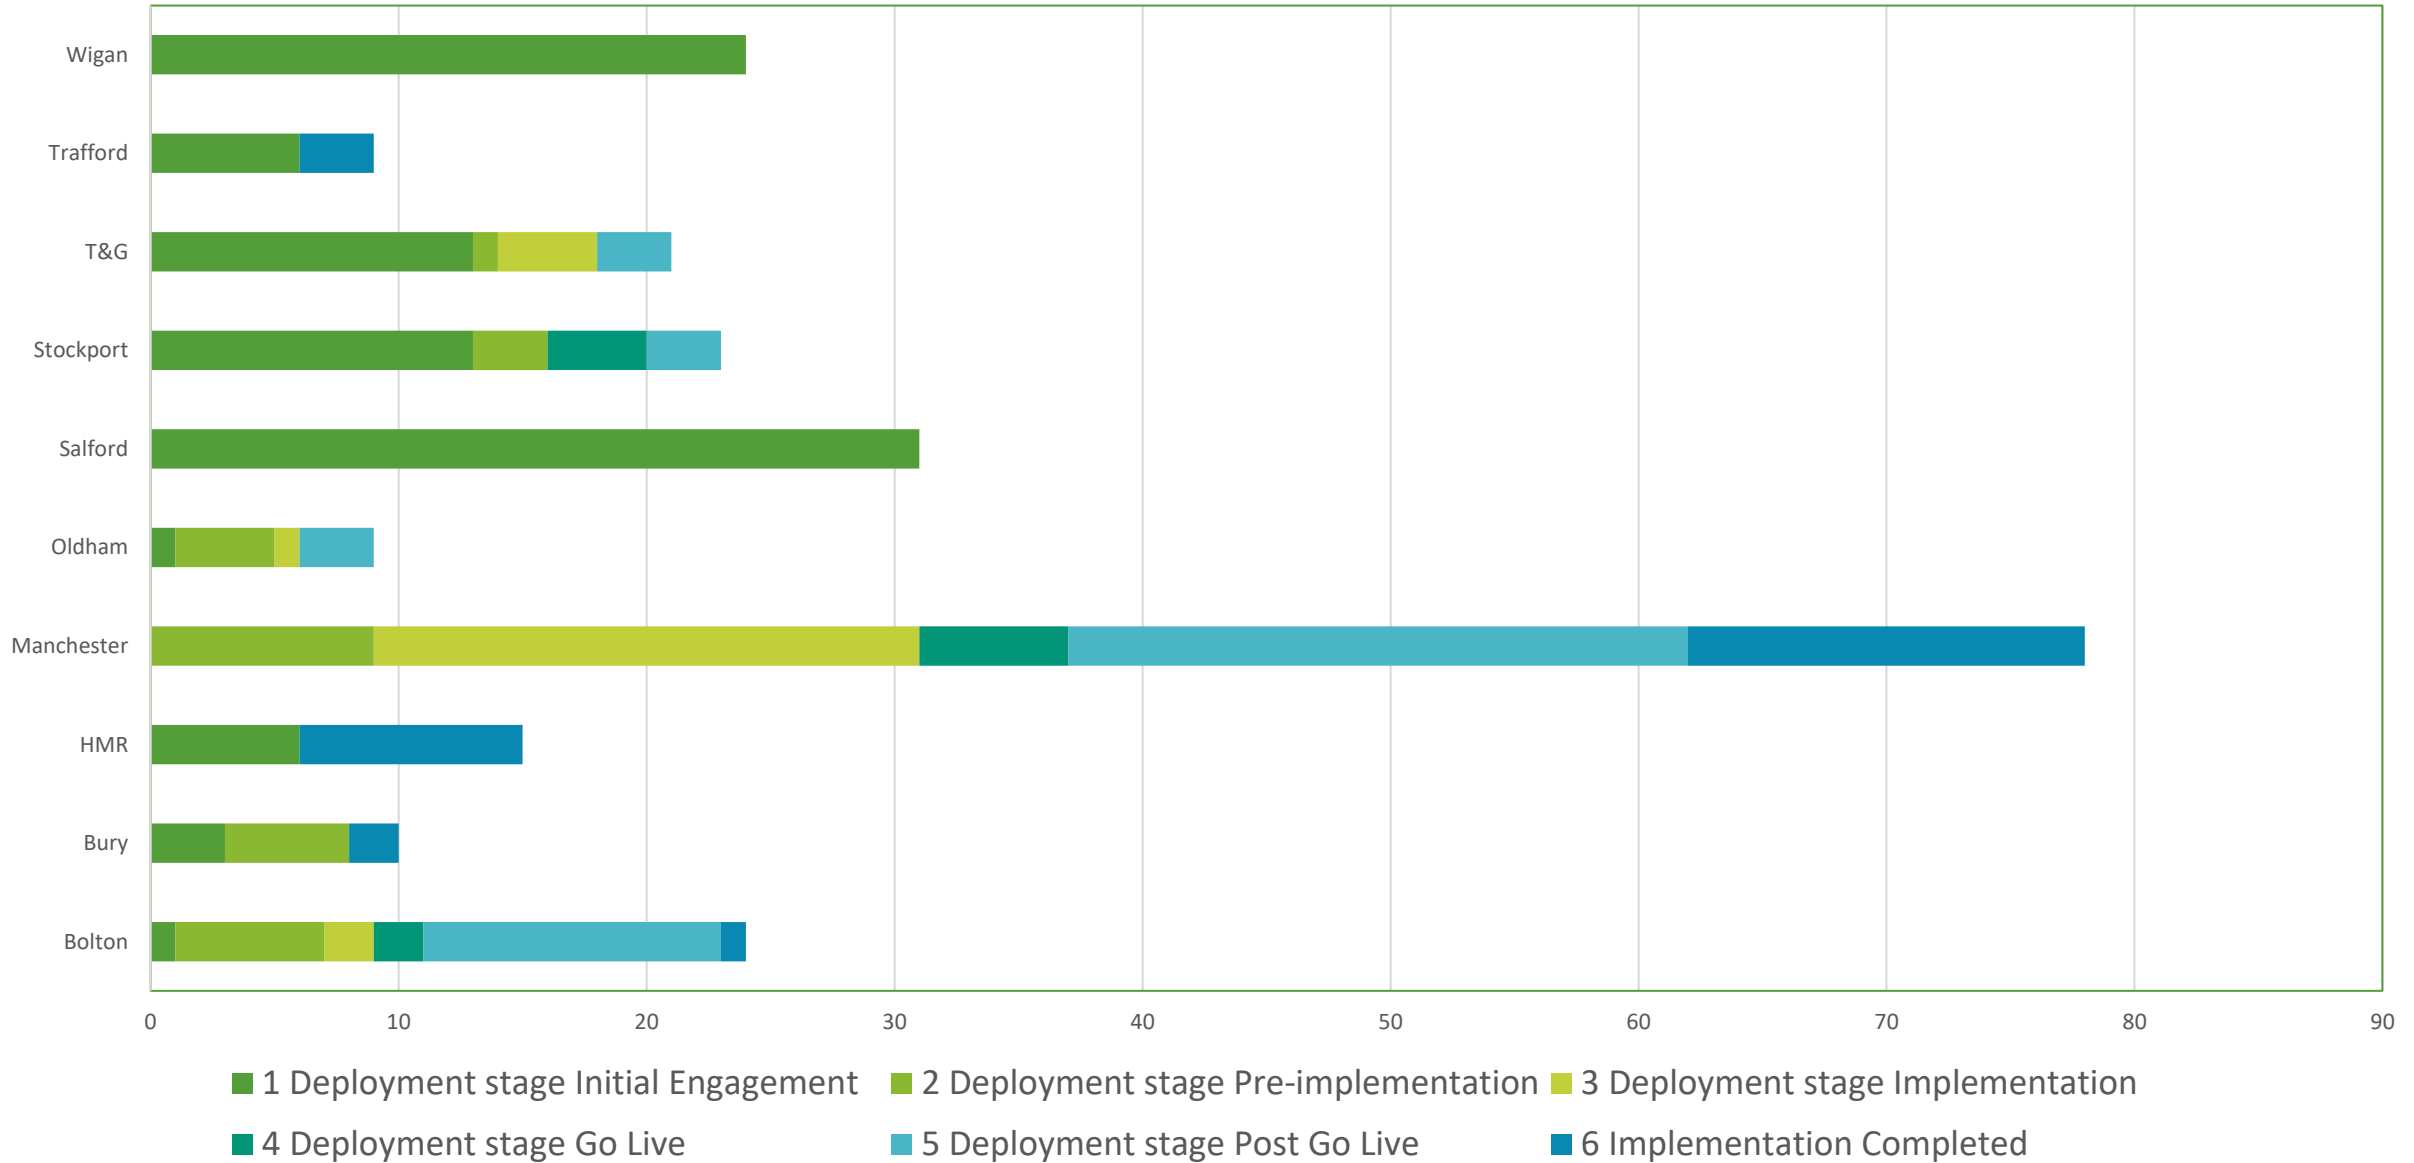

# Age of referred patients



# Presenting complaint

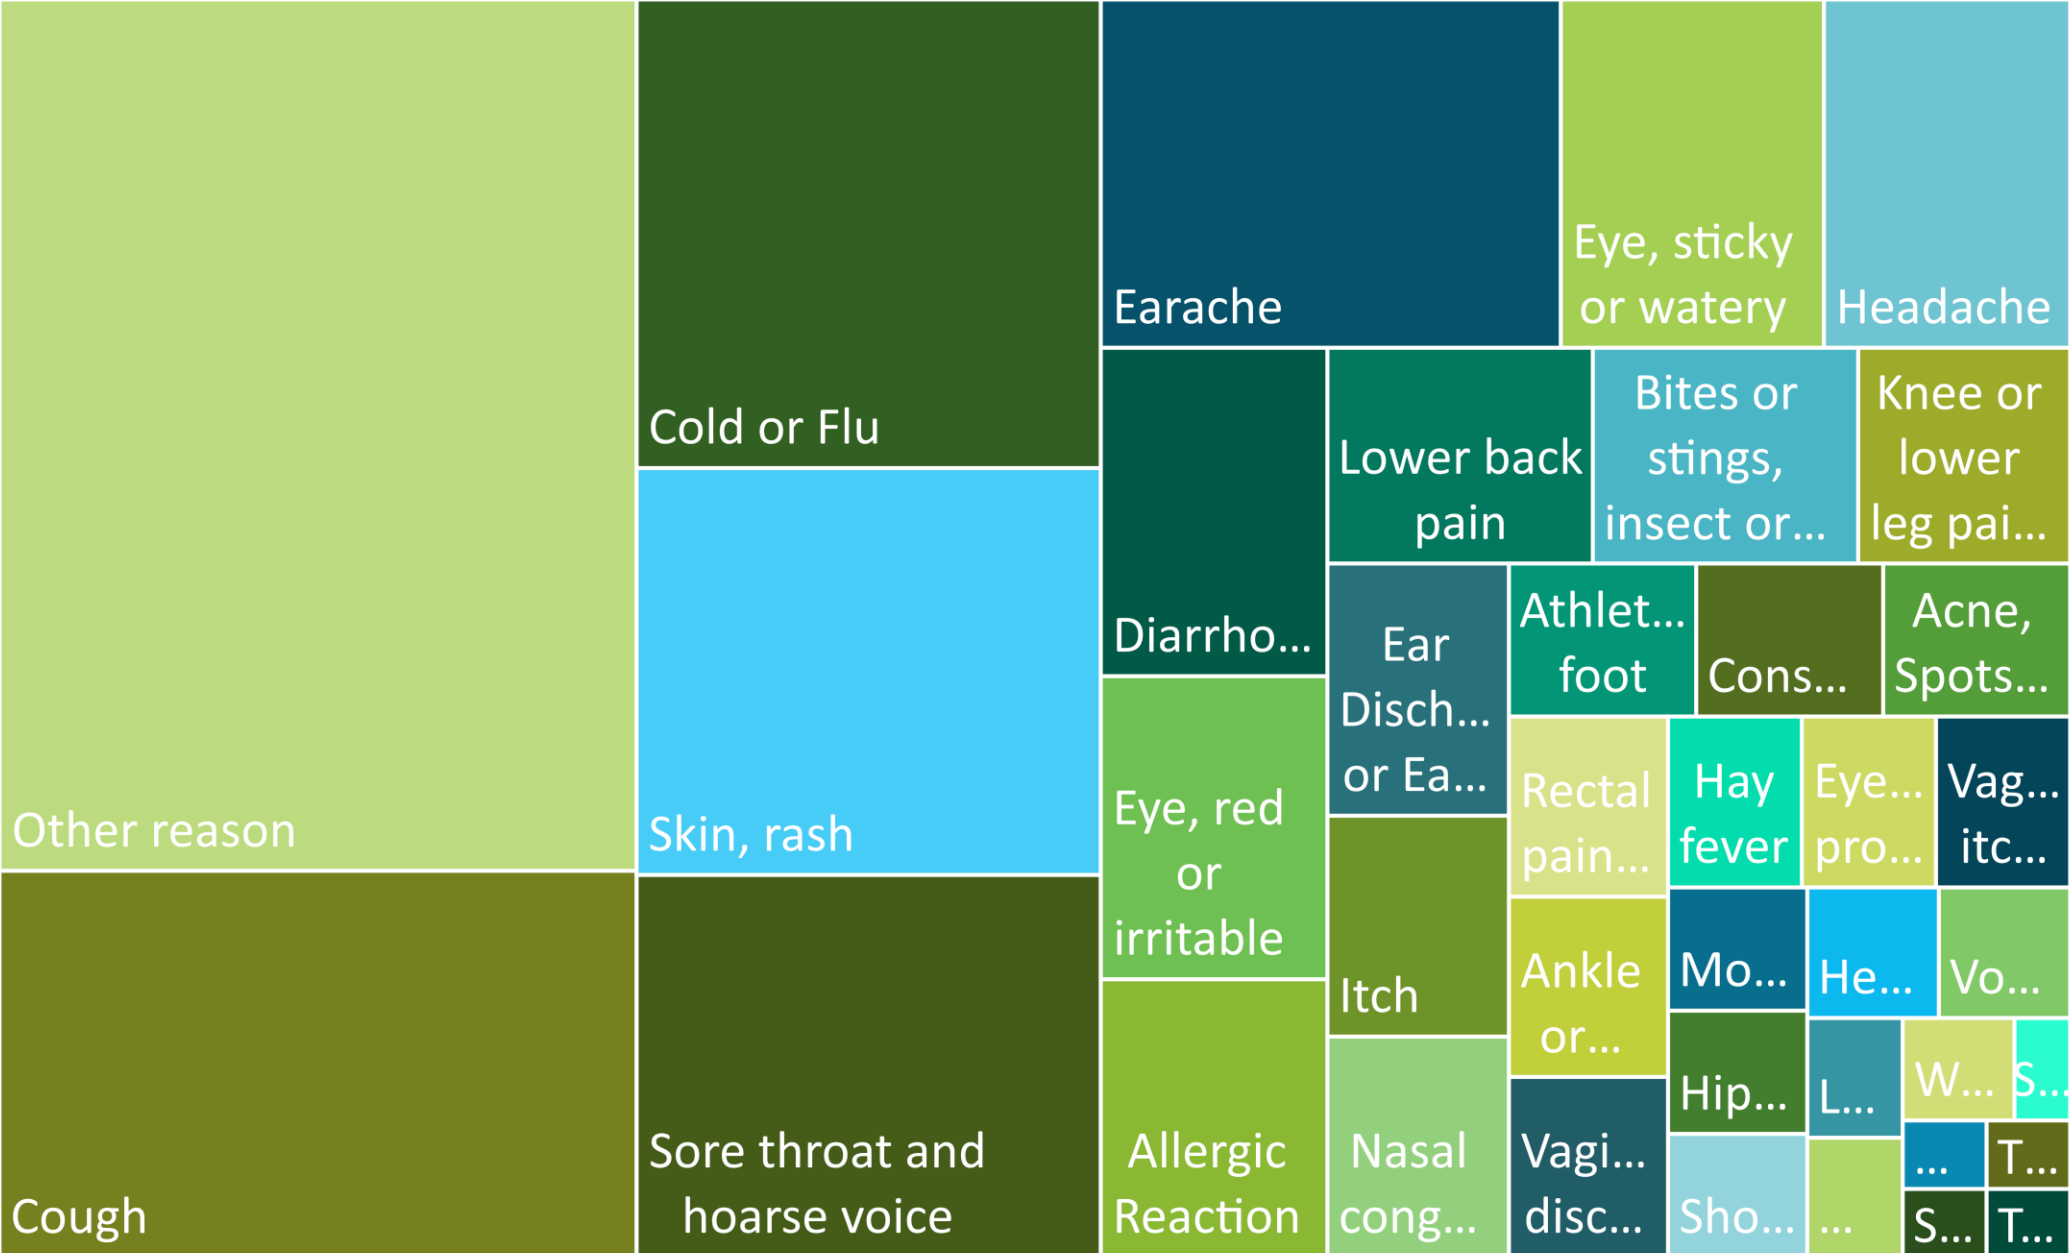

Looking ahead to next month



# Activities Planned for October:

Governance	Project Management	Engagement	Deployment
<ul style="list-style-type: none"><li>• PMO funding situation confirmed</li><li>• Primary Care Accelerator bid update</li><li>• Confirmation of forecast financial position at year end</li><li>• Liaise with general practice colleagues re practices live but not referring</li></ul>	<ul style="list-style-type: none"><li>• Review deployment blueprint</li><li>• Discuss pharmacy access to CCG-funded translation services for GP CPCS with 9 localities</li><li>• Consider where IIF details fits in the deployment blueprint &amp; update as appropriate</li><li>• c/f Plan activity reporting to all PCNs with GMHSCP</li></ul>	<ul style="list-style-type: none"><li>• c/f Update to GPPB</li><li>• GM association of LMCs</li><li>• Arrange RPS-supported CPCS training sessions for community pharmacy</li></ul>	<ul style="list-style-type: none"><li>• Support set-up of PharmOutcomes / Outcomes 4 Health logins for live practices re access to data and reporting &amp; then confirm to practices how to access</li></ul>

# GM Locality Deployment Detail

Bolton: [louise@boltonlpc.org.uk](mailto:louise@boltonlpc.org.uk)

Practice code	Practice Name	Deployment stage
P82030	Deane Medical Centre	1 Deployment stage Initial Engagement
P82633	Great Lever One	4 Deployment stage Go Live
P82036	Dr Subramanian	2 Deployment stage Pre-implementation
P82020	Dr C Hallikeri	2 Deployment stage Pre-implementation
P82011	Dr J Lowe & Partners (Tonge Fold)	4 Deployment stage Go Live
p82001	The Dunstan Partnership	5 Deployment stage Post Go Live
P82018	Dr A Ariff & Partners (Alastair Ross)	5 Deployment stage Post Go Live
P82010	Dalefield Surgery	5 Deployment stage PostGo Live
P82014	Spring House	5 Deployment stage Post Go Live
P82031	Heaton Medical Centre	5 Deployment stage Post Go Live
P82627	Cornerstone surgery	4 Deployment stage Go Live
P82634	Dr James-Authe & Partner (Wyresdale Surgery)	5 Deployment stage Post Go Live
P82007	Kearsley Medical Centre	5 Deployment stage Post Go Live
p82008	Stonehill	5 Deployment stage Post Go Live
Y03079	Bolton Community Practice	5 Deployment stage Post Go Live
P82022	Dr C Hendy & Partner	2 Deployment stage Pre-implementation
P82012	Dr Earnshaw & Partners (Lever Chambers 1)	3 Deployment stage Implementation
P82029	Dr M Jeyam & Partner	5 Deployment stage Post Go Live
P82626	Dr Uddin & Partners	5 Deployment stage Post Go Live
P82002	Dr Mirza (Pikes Lane 1)	2 Deployment stage Pre-implementation
P82009	Garnet Fold Practice	5 Deployment stage Post Go Live
P82004	Swan Lane	6 Implementation Completed
P82016	Harwood Medical Centre	2 Deployment stage Pre-implementation
P82643	Dr S N Liversedge & Partners	2 Deployment stage Pre-implementation

Bury: [alison@cpgmhealthcare.co.uk](mailto:alison@cpgmhealthcare.co.uk)  
[luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
P83015	Ribblesdale Medical Practices	6 Implementation Completed
P83020	Minden Medical Centre - Saxena	1 Deployment stage Initial Engagement
P83612	Mile Lane Health Centre	1 Deployment stage Initial Engagement
P83012	Tower Family Healthcare	2 Deployment stage Pre-implementation
P83017	Woodbank MC	2 Deployment stage Pre-implementation
P83603	Redbank Health Centre	6 Implementation Completed
P83605	Whittaker Lane Medical Centre	1 Deployment stage Initial Engagement
P83004	Uplands Medical Centre	2 Deployment stage Pre-implementation
P83009	Blackford House Medical Centre	1 Deployment stage Initial Engagement
P83011	Unsworth Medical Centre	2 Deployment stage Pre-implementation
P83608	The Elms Medical Centre	2 Deployment stage Pre-implementation

HMR: [luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
P86007	Dr Caldwell & Partners	6 Implementation Completed
P86009	Dr Bodner & Partners	6 Implementation Completed
Y02720	The Kingsway Practice	6 Implementation Completed
Y02721	Kirkholt Medical Practice	6 Implementation Completed
P86011	Longford Street Group Practice	6 Implementation Completed
P86016	Heywood Health	6 Implementation Completed
P86023	Dr Osborne & Partner	6 Implementation Completed
P86602	Heady Hill Surgery	6 Implementation Completed
Y02718	Birtle View Medical Practice	6 Implementation Completed
P86002	Vicar's Drive Surgery (Dr Bhima)	1 Deployment stage Initial Engagement
P86014	Dr Babar & Partners	1 Deployment stage Initial Engagement
P86606	Dr Swamy & Partner	1 Deployment stage Initial Engagement
P86609	The Dale Medical Practice	1 Deployment stage Initial Engagement
P86614	Dr Hamid	1 Deployment stage Initial Engagement
P86619	Dr Ghafoor & Partner	1 Deployment stage Initial Engagement

# Manchester p1:[luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
P84005	The Vallance Centre	6 Implementation Completed
P84009	Ailsa Craig Medical Group	6 Implementation Completed
P84023	Surrey Lodge Group Practice	6 Implementation Completed
P84026	Dickenson Road Medical Centre	6 Implementation Completed
P84037	The Ardwick Medical Practice - prev Dr Cunningham	6 Implementation Completed
P84611	Drs Chiu, Koh & Gan	6 Implementation Completed
P84626	Wilmslow Road Medical Centre	6 Implementation Completed
P84644	Parkside Surgery	6 Implementation Completed
P84689	Longsight Medical Practice	6 Implementation Completed
P84030	Collegiate Medical Centre	2 Deployment stage Pre-implementation
P84046	Cheetham Hill Primary Care Centre	2 Deployment stage Pre-implementation
P84074	Wellfield Medical Centre	2 Deployment stage Pre-implementation
P84640	Queens Medical Centre	2 Deployment stage Pre-implementation
P84645	Park View Medical Centre	2 Deployment stage Pre-implementation
P84663	The Neville Family Medical Centre	2 Deployment stage Pre-implementation
P84684	Jolly Medical Centre	2 Deployment stage Pre-implementation
P84064	New Islington Medical Practice	5 Deployment stage Post Go Live
P84673	Urban Village Medical Practice	3 Deployment stage Implementation
Y02849	City Health Centre	6 Implementation Completed
P84041	Cornerstones Family Practice	5 Deployment stage Post Go Live
P84051	Eastlands Medical Practice, Clayton Health Centre	5 Deployment stage Post Go Live
P84059	Lime Square Medical Centre	5 Deployment stage Post Go Live
P84004	Five Oaks Family Practice	6 Implementation Completed
P84032	Clayton Health Centre	6 Implementation Completed
P84042	Florence House Medical Practice	6 Implementation Completed
P84637	Clayton Health Centre	5 Deployment stage Post Go Live
P84022	Kingsway Medical Practice	3 Deployment stage Implementation
P84034	Barlow Medical Centre	4 Deployment stage Go Live
P84066	David Medical Centre	4 Deployment stage Go Live
P84678	Didsbury Medical Centre	3 Deployment stage Implementation
P84016	Levenshulme Health Centre	5 Deployment stage Post Go Live

# Manchester p2: [luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

P84027	West Point Medical Centre	5 Deployment stage Post Go Live	M19 2AF Manchester	Gorton & Levenshulme
P84028	Gorton Medical Centre	3 Deployment stage Implementation	M18 8LI Manchester	Gorton & Levenshulme
P84050	Mount Road Surgery	5 Deployment stage Post Go Live	M18 7BQ Manchester	Gorton & Levenshulme
P84052	West Gorton Medical Practice	4 Deployment stage Go Live	M12 5JE Manchester	Gorton & Levenshulme
P84053	Ashcroft Surgery	4 Deployment stage Go Live	M19 3BS Manchester	Gorton & Levenshulme
Y02890	The Hawthorn Medical Centre	4 Deployment stage Go Live	M14 6FS Manchester	Gorton And Levenshulme
P84605	Fernclough Surgery	2 Deployment stage Pre-implementation	M9 5RD Manchester	H-Blackley Harpurhey & Charlestown
P84679	Willowbank Surgery	2 Deployment stage Pre-implementation	M9 4WH Manchester	H-Blackley Harpurhey & Charlestown
P84616	Manchester Medical	6 Implementation Completed	M14 4GP Manchester	Hulme Moss Side Rusholme & City Centre South
P84669	Cornbrook Medical Practice	6 Implementation Completed	M15 4EA Manchester	Hulme Moss Side Rusholme & City Centre South
P84630	The Arch MP Hulme Medical Centre	6 Implementation Completed	M15 5TJ Manchester	Hulme Moss Side Rusholme & City Centre South
P84683	The Docs	5 Deployment stage Post Go Live	M1 3LY Manchester	Hulme Moss Side Rusholme & City Centre South
P84025	St Georges Medical Centre	5 Deployment stage Post Go Live	M40 5HP Manchester	Miles Platting, Newton Heath & Moston
P84047	Droylsden Road Family Practice	3 Deployment stage Implementation	M40 1NT Manchester	Miles Platting, Newton Heath & Moston
P84054	Whitley Road Medical Centre	5 Deployment stage Post Go Live	M40 7QH Manchester	Miles Platting, Newton Heath & Moston
P84067	Hazeldene Medical Centre	3 Deployment stage Implementation	M40 3HD Manchester	Miles Platting, Newton Heath & Moston
P84070	Newton Heath Health Centre	3 Deployment stage Implementation	M40 2JF Manchester	Miles Platting, Newton Heath & Moston
Y01695	Victoria Mill Medical Practice	3 Deployment stage Implementation	M40 7LJ Manchester	Miles Platting, Newton Heath & Moston
Y02520	Simpson Medical Practice	3 Deployment stage Implementation	M40 9NB Manchester	Miles Platting, Newton Heath & Moston
P84012	Northenden Group Practice	5 Deployment stage Post Go Live	M22 4DH Manchester	Northenden & Brooklands (Wythenshawe)
P84651	Northern Moor Medical Centre	5 Deployment stage Post Go Live	M23 0PH Manchester	Northenden & Brooklands (Wythenshawe)
P84045	Park Medical Centre	5 Deployment stage Post Go Live	M23 9AB Manchester	Northenden & Brooklands (Wythenshawe)
P84672	Woodlands Medical Practice	5 Deployment stage Post Go Live	M23 9RL Manchester	Northenden & Brooklands (Wythenshawe)
P84061	Brooklands Medical Practice	5 Deployment stage Post Go Live	M23 9JH Manchester	Northenden & Brooklands (Wythenshawe)
P84072	The Robert Darbshire Practice Ltd.	3 Deployment stage Implementation	M14 5NP Manchester	Robert Darbshire Practice
P84635	The Whitswood Practice	3 Deployment stage Implementation	M16 7AP Manchester	Robert Darbshire Practice
Y02960	New Bank Health Centre	4 Deployment stage Go Live	M12 4EY Manchester	Robert Darbshire Practice

# Manchester p3:[luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

P84038	Ashville Surgery	5 Deployment stage Post Go Live
P84039	The Range Medical Centre	3 Deployment stage Implementation
P84056	Princess Road Surgery	3 Deployment stage Implementation
P84068	Chorlton Family Practice	3 Deployment stage Implementation
P84071	Wilbraham Surgery	5 Deployment stage Post Go Live
P84650	The Alexandra Practice	3 Deployment stage Implementation
P84652	Corkland Road Medical Practice	3 Deployment stage Implementation
P84010	Borchardt Medical Centre	3 Deployment stage Implementation
P84017	Ladybarn Group Practice	3 Deployment stage Implementation
P84018	Mauldeth Medical Centre	3 Deployment stage Implementation
P84035	Bodey Medical Centre	5 Deployment stage Post Go Live
P84639	Fallowfield Medical Practice	5 Deployment stage Post Go Live
P84665	Al-Shifa Medical Centre	5 Deployment stage Post Go Live
P84014	RK Medical Practice	3 Deployment stage Implementation
P84020	Peel Hall Medical Practice	5 Deployment stage Post Go Live
P84021	The Maples Medical Centre	5 Deployment stage Post Go Live
P84024	Bowland Medical Practice	5 Deployment stage Post Go Live
P84029	Benchill Medical Practice	5 Deployment stage Post Go Live
P84043	Cornishway Group Practice	3 Deployment stage Implementation
P84048	Tregenna Group Practice	3 Deployment stage Implementation



Oldham: [alison@cpgmhealthcare.co.uk](mailto:alison@cpgmhealthcare.co.uk)  
[luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
P85014	Hopwood House Medical Practice	1 Deployment stage Initial Engagement
P85011	CH Medical	2 Deployment stage Pre-implementation
P85028	Block Lane Surgery	2 Deployment stage Pre-implementation
P85605	Littletown Family Medical Practice	2 Deployment stage Pre-implementation
P85612	Werneth Medical Practice	2 Deployment stage Pre-implementation
P85004	Dr Akhter & Partners	3 Deployment stage Implementation
p85010	Woodlands Medical Practice	5 Deployment stage Post Go Live
P85018	Dr Danson	5 Deployment stage Post Go Live
P85615	Kapur Family Care	5 Deployment stage Post Go Live

Salford: [rikki@gmlpc.org.uk](mailto:rikki@gmlpc.org.uk)  
[luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
P87020	Dr Budden & Partners	1 Deployment stage Initial Engagement
P87024	Dr Tamkin & Partners	1 Deployment stage Initial Engagement
P87610	Dr Hope & Partners	1 Deployment stage Initial Engagement
P87620	Dr Borg-Costanzi & Partners	1 Deployment stage Initial Engagement
P87649	Dr Joshi & Partner	1 Deployment stage Initial Engagement
P87657	Salford Care Centres Irlam	1 Deployment stage Initial Engagement
Y00445	Salford Primary Care Together	1 Deployment stage Initial Engagement
P87004	Dr A Salim & Partner	1 Deployment stage Initial Engagement
P87015	Dr M Austin & Partner	1 Deployment stage Initial Engagement
P87027	Dr Haber & Partners	1 Deployment stage Initial Engagement
P87032	Dr V B Raj & Partner	1 Deployment stage Initial Engagement
P87035	Dr Saxby & Partners	1 Deployment stage Initial Engagement
P87040	Dr N A Finegan & Partners	1 Deployment stage Initial Engagement
P87634	Dr J W Tankel & Partners	1 Deployment stage Initial Engagement
P87639	Salford Care Centres Weaste	1 Deployment stage Initial Engagement
P87658	Dr J Y Amin	1 Deployment stage Initial Engagement
Y02767	The Height General Practice	1 Deployment stage Initial Engagement
P87002	Dr J Harris & Partners	1 Deployment stage Initial Engagement
P87016	Dr G K Jolly & Partners	1 Deployment stage Initial Engagement
p87019	Silverdale Medical Practice	1 Deployment stage Initial Engagement
P87025	Dr Stedman & Partners	1 Deployment stage Initial Engagement
P87008	Dr B Sutherland & Partners	1 Deployment stage Initial Engagement
P87017	Dr D K Mccarthy & Partners	1 Deployment stage Initial Engagement
P87028	Dr Browne & Partners	1 Deployment stage Initial Engagement
P87613	Dr U I N Umeadi & Partner	1 Deployment stage Initial Engagement
P87618	Dr Y Loomba	1 Deployment stage Initial Engagement
P87624	Dr S Mccorkindale & Partners	1 Deployment stage Initial Engagement
P87625	Dr A Ahuja	1 Deployment stage Initial Engagement
P87627	Dr Nagesh Chennupati	1 Deployment stage Initial Engagement
P87630	Cherry Medical Practice	1 Deployment stage Initial Engagement
P87661	Dr M T Khan	1 Deployment stage Initial Engagement

Stockport: [rikki@gmlpc.org.uk](mailto:rikki@gmlpc.org.uk)  
[luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
P88025	Dr Shipston AM & Partners	1 Deployment stage Initial Engagement
P88020	Cheadle Medical Practice	4 Deployment stage Go Live
P88023	Heald Green Health Centre 2	4 Deployment stage Go Live
P88024	Gatley Medical Centre	4 Deployment stage Go Live
P88042	Heald Green Health Centre 1	4 Deployment stage Go Live
P88002	Dr Hedley PJ & Partners	1 Deployment stage Initial Engagement
P88006	Heaton Norris Health Centre	1 Deployment stage Initial Engagement
P88012	Heaton Norris Health Centre	1 Deployment stage Initial Engagement
P88021	Dr Valluri & Partners	1 Deployment stage Initial Engagement
P88606	Dr Aldabbagh	1 Deployment stage Initial Engagement
P88623	Dr Mathewson RCL & Partners	1 Deployment stage Initial Engagement
P88005	Family Surgery	2 Deployment stage Pre-implementation
P88011	Heaton Norris Health Centre	2 Deployment stage Pre-implementation
P88018	Park View Group Practice	5 Deployment stage Post Go Live
P88043	Brinnington Health Centre	5 Deployment stage Post Go Live
P88610	South Reddish Medical Centre	5 Deployment stage Post Go Live
P88615	Vernon Park Surgery	2 Deployment stage Pre-implementation
P88009	South Reddish Medical Centre	1 Deployment stage Initial Engagement
P88017	Dr Spreckley DE & Partners	1 Deployment stage Initial Engagement
P88019	The Alvanley Family Practice	1 Deployment stage Initial Engagement
P88044	Dr Armstrong MH & Partners	1 Deployment stage Initial Engagement
P88607	Dr Patel R & Partner	1 Deployment stage Initial Engagement
P88625	Dr Parker G & Partners	1 Deployment stage Initial Engagement

T&G: [alison@cpgmhealthcare.co.uk](mailto:alison@cpgmhealthcare.co.uk)  
[luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
p89020	HT PRACTICE	1 Deployment stage Initial Engagement
P89010	Medlock Vale Medical Practice	1 Deployment stage Initial Engagement
P89015	Millgate Healthcare Partnership	2 Deployment stage Pre-implementation
P89018	Denton Medical Practice	3 Deployment stage Implementation
P89002	The Brooke Surgery	1 Deployment stage Initial Engagement
P89004	Awburn House Surgery	1 Deployment stage Initial Engagement
P89012	Clarendon Medical Centre	1 Deployment stage Initial Engagement
P89013	Hattersley Group Practice	1 Deployment stage Initial Engagement
P89014	Haughton Thornley Medical Centres	1 Deployment stage Initial Engagement
P89016	Donneybrook Medical Centre	1 Deployment stage Initial Engagement
P89021	Dukinfield Medical Centre	1 Deployment stage Initial Engagement
P89602	The Smithy Surgery	1 Deployment stage Initial Engagement
P89026	Grosvenor Medical Centre	1 Deployment stage Initial Engagement
P89612	Mossley Medical Practice	1 Deployment stage Initial Engagement
P89618	The Pike Medical Centre	1 Deployment stage Initial Engagement
P89022	King Street Medical Centre	3 Deployment stage Implementation
P89023	St. Andrews House	3 Deployment stage Implementation
Y02936	Millbrook Medical Practice	3 Deployment stage Implementation
P89005	Lockside Medical Centre	5 Deployment stage Post Go Live
P89007	Staveleigh Medical Centre	5 Deployment stage Post Go Live
P89025	Town Hall Surgery	5 Deployment stage Post Go Live

Trafford: [luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
P91006	The Urmston Group Practice	6 Implementation Completed
P91009	Davyhulme Medical Centre	6 Implementation Completed
P91012	Primrose Surgery	6 Implementation Completed
P91013	Boundary House Medical Centre	1 Deployment stage Initial Engagement
P91014	Washway Road Medical Centre	1 Deployment stage Initial Engagement
P91017	Bodmin Road Health Centre	1 Deployment stage Initial Engagement
P91020	Brooks Bar Medical Centre	1 Deployment stage Initial Engagement
P91021	Firsway Health Centre	1 Deployment stage Initial Engagement
P91035	Conway Road Health Centre	1 Deployment stage Initial Engagement

Wigan: [luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage
P92007	Wong & Partners	1 Deployment stage Initial Engagement
P92023	Brookmill Medical Centre	1 Deployment stage Initial Engagement
P92029	Westleigh Medical Practice	1 Deployment stage Initial Engagement
P92035	Lilford Park Surgery	1 Deployment stage Initial Engagement
P92602	Foxleigh Family Surgery	1 Deployment stage Initial Engagement
P92607	Grasmere Surgery	1 Deployment stage Initial Engagement
P92615	The Avenue Surgery	1 Deployment stage Initial Engagement
P92621	Premier Health	1 Deployment stage Initial Engagement
Y00050	Pennington Park Surgery	1 Deployment stage Initial Engagement
Y02322	Leigh Family Practice	1 Deployment stage Initial Engagement
Y02886	Leigh Sports Village	1 Deployment stage Initial Engagement
P92010	Beech Hill Medical Practice	1 Deployment stage Initial Engagement
P92014	Standish Medical Practice	1 Deployment stage Initial Engagement
P92015	Aspull Surgery	1 Deployment stage Initial Engagement
P92017	Shevington Surgery	1 Deployment stage Initial Engagement
P92003	The Dicconson Group Practice	1 Deployment stage Initial Engagement
P92008	Suntha & Partners	1 Deployment stage Initial Engagement
P92011	Smith & Partners	1 Deployment stage Initial Engagement
P92019	Pemberton Surgery	1 Deployment stage Initial Engagement
P92021	Drs D'Arifat, Elislam, Wan & Shaikh	1 Deployment stage Initial Engagement
P92026	Patel, Kamath & Partners	1 Deployment stage Initial Engagement
P92030	Dr Seabrook & partner	1 Deployment stage Initial Engagement
P92634	Ellis & Partner	1 Deployment stage Initial Engagement
Y02885	Marsh Green Medical Practice	1 Deployment stage Initial Engagement
