

GP CPCS  
Report:  
November 2021

8<sup>th</sup> December 2021



**Greater Manchester  
Community Pharmacy**  
Provider Board

# GP CPCS Highlights: November

72% (310) GM practices engaged or live

108 practices trained & live, 80 actively referring

148 of 353 practices completed MS form

43% referrals advice only

26% referrals for children aged 1-9

Top 3 referral reasons: cough, skin rash, sore throat

# October Update

## Governance

- EMIS procurement:
  - Detailed deployment plan breakdown shared with EMIS to be included in the contract
  - EMIS confirm that the final SBS contract will be ready by the end of November but not received
  - GMSS considering mitigation for any delays, urgent work required in December to address the issue
- Project funding:
  - Year 2 EMIS licence fees - agreed to be covered by GMHSCP primary care team
  - PMO funding - confirmation from NW region of an additional ~£60k funding to support deployment – funds not received in November
  - CHL funding for Dec to Mar agreed by LB to ensure continuity of PMO support
  - Forecast spend to year end calculated and shared with GMHSCP
  - SLA arrangements to support funding flows discussed, finalise to December
- Monthly meetings with LB as SRO, GMHSCP finance & GMSS continue
- EMIS app and PharmRefer functionality updates confirmed
- IIF / WPAF:
  - Agreed to combine pre-implementation & GP commitment forms into one and adopt as the form for practices to complete to satisfy requirements
  - Comms agreed
  - Sent to all practices not currently actively referring (353) by heads of primary care in each of 10 CCGs with deadline for response on 1<sup>st</sup> Dec and breakdown per locality of practices to send to
  - 'sign up and make full use of' wording in WPAF needs further clarification from GM as to interpretation

## Engagement

- Community pharmacy best practice webinar agreed to be planned for January
- GPPB update provided with positive reception on progress made in deployment
- RPS training for CPCS for pharmacists took place on Tues 23<sup>rd</sup> and Tues 30<sup>th</sup> November

## Project Planning

- GMHSCP new role in place in November providing PMO support to community pharmacy services as part of transformation team. CR provided significant support with the IIF/WPAF comms and also has committed to support with the preparation and distribution of monthly activity reports out to localities and PCNs
- Status of all practices in deployment plan wrt EMIS activation provided by EMIS and added to deployment plan. 79 practices made live by EMIS but no go live date agreed. Prioritise these practices to get go live dates agreed ASAP
- Proposal to switch on all practices for EMIS/PharmRefer in January so this is not a barrier to go live discussed & agreed in principle – further discussions in December
- Deployment plan updated daily based on responses to MS form
- Amendment to deployment blueprint following issues with practices attending training but not having a go live date agreed
- Locality leads reviewed and confirmed:
  - Alison = Bury, Oldham, Tameside
  - Luvjit = Manchester, Trafford, Wigan
  - Rikki = HMR, Salford, Stockport
  - Louise = Bolton
- Concerns raised about practices starting to make referrals without going through the deployment process – agreed comms needed to mitigate
- Deployment blueprint reviewed to consolidate engagement and pre-implementation stages following introduction of MS form. Full review of process and all supporting documents, with new templates prepared ready for review & sign off by working group
- 'Dos and Don'ts' reviewed and updated based on GP feedback
- All pharmacy mapping completed for practices in the deployment plan prior to IIF/WPAF comms being sent
- Annex C data updated in PharmOutcomes

## Deployment

- 11 practices went live in November
- Total 108 practices live, 80 actively referring
- Post-deployment work continues with daily support to community pharmacies and regular ad hoc support to general practices – resource to continue this essential work flagged to GMHSCP and is of concern due to capacity issues. GMHSCP direct involvement with any pharmacies of concern agreed
- Drop-in support sessions for live general practices and pharmacies agreed – will be set up to commence fortnightly calls in January


Deployment update

# Deployment Overview

Status Date: 3/12/2021

Number of General Practices in Deployment by Deployment Status

Deployment Stage	Number of Practices	% of GM practices
1 Initial Engagement	41	10%
2 Pre Implementation	37	9%
3 Implementation	121*	28%
4 Go Live	2	0.5%
5 Post Go Live	8	2%
6 Implementation complete	101	23%

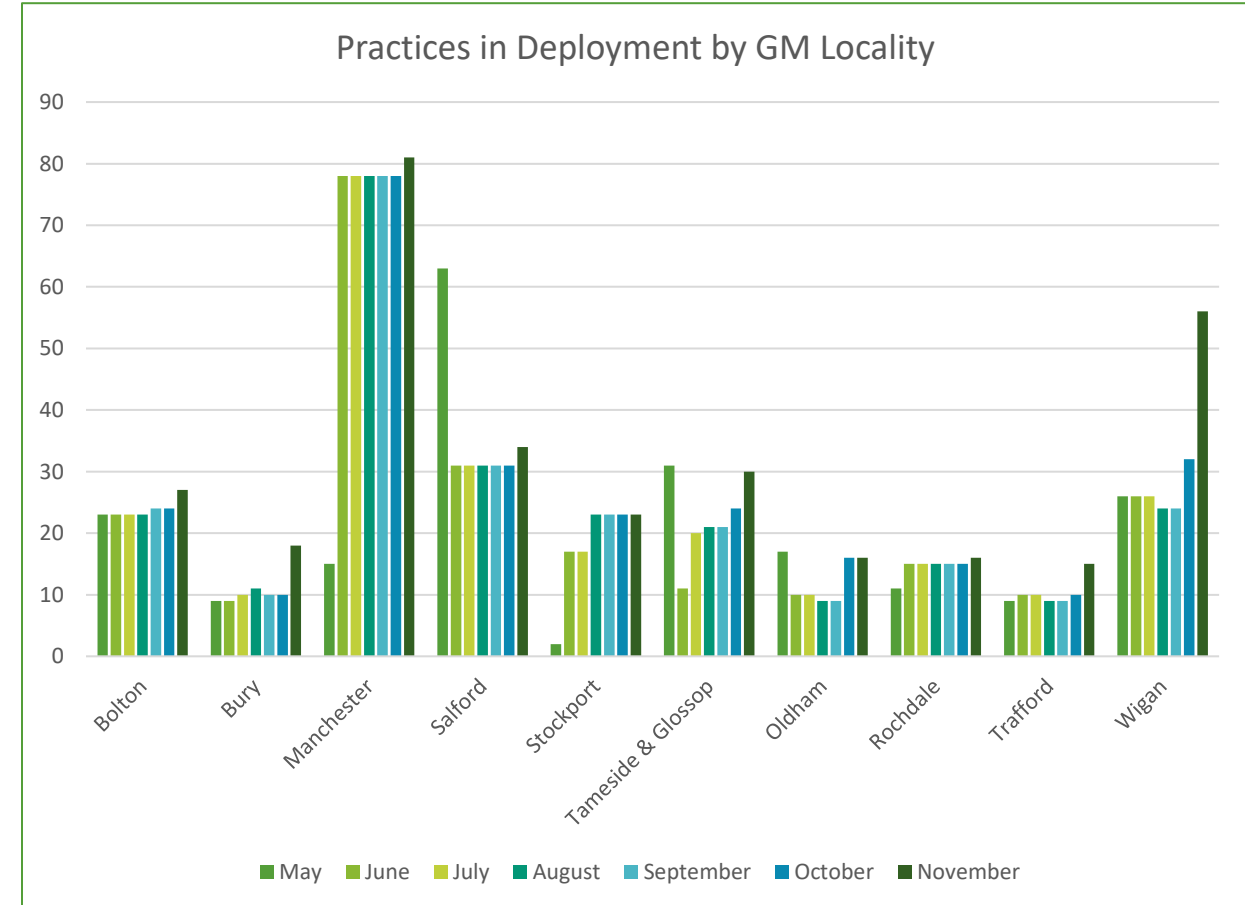

**310 (72%) of GM General Practices are currently in deployment**

\* All practices who completed the MS form sent out in November for WPAF / IIF move straight into stage 3 implementation, having agreed to go live and supplied pre-implementation information.

# Deployment Overview by CCG

CCG	Practices in CCG	% Practices engaged	% Practices Trained	% Practices Live
Bolton	49	55%	39%	37%
Bury	26	62%	12%	12%
HMR	36	44%	25%	25%
Manchester	85	94%	64%	61%
Oldham	39	41%	18%	18%
Salford	38	84%	5%	0%
Stockport	36	64%	28%	28%
T&G	37	81%	8%	8%
Trafford	27	56%	15%	15%
Wigan	58	95%	0%	0%

# Deployment Activity

Number of training sessions delivered	Number of attendees	Number of practices represented
8	75	18

## Deployment Resource\*:

Bolton LPC: 28 hours (n=1)

CHL hours: 97 hours (n=2)

GMLPC: 124 hours (n=2)

PCB: 45 hours (n=1)

## Deployment update:

In late November, a communication was sent out to all GM general practices from the Heads of Primary Care at each CCG to ask practices to confirm their intentions around engagement with the GP Community Pharmacist Consultation Service (GP CPCS).

A MS form was prepared to capture this information and a deadline of 1<sup>st</sup> December given for completion. As of 1<sup>st</sup> December, 148 of the 353 practices needing to complete the form had done so (live and active practices were not required to submit the form).


The data collected from this form will be used to inform the requirements for the Winter Primary Care Access Fund for general practice and for the PCN Investment and Impact Fund.

## Wigan Update:

Significant engagement work has also been completed in October and November in Wigan, which now has 97% of practices engaged.

\*LPC resource is provided from core LPC funding (contractual levy from pharmacy contractors) – no additional funding has been received to deploy GP CPCS.  
CHL resource for November agreed from minimal existing project funds held.

# Live vs. Active Practices

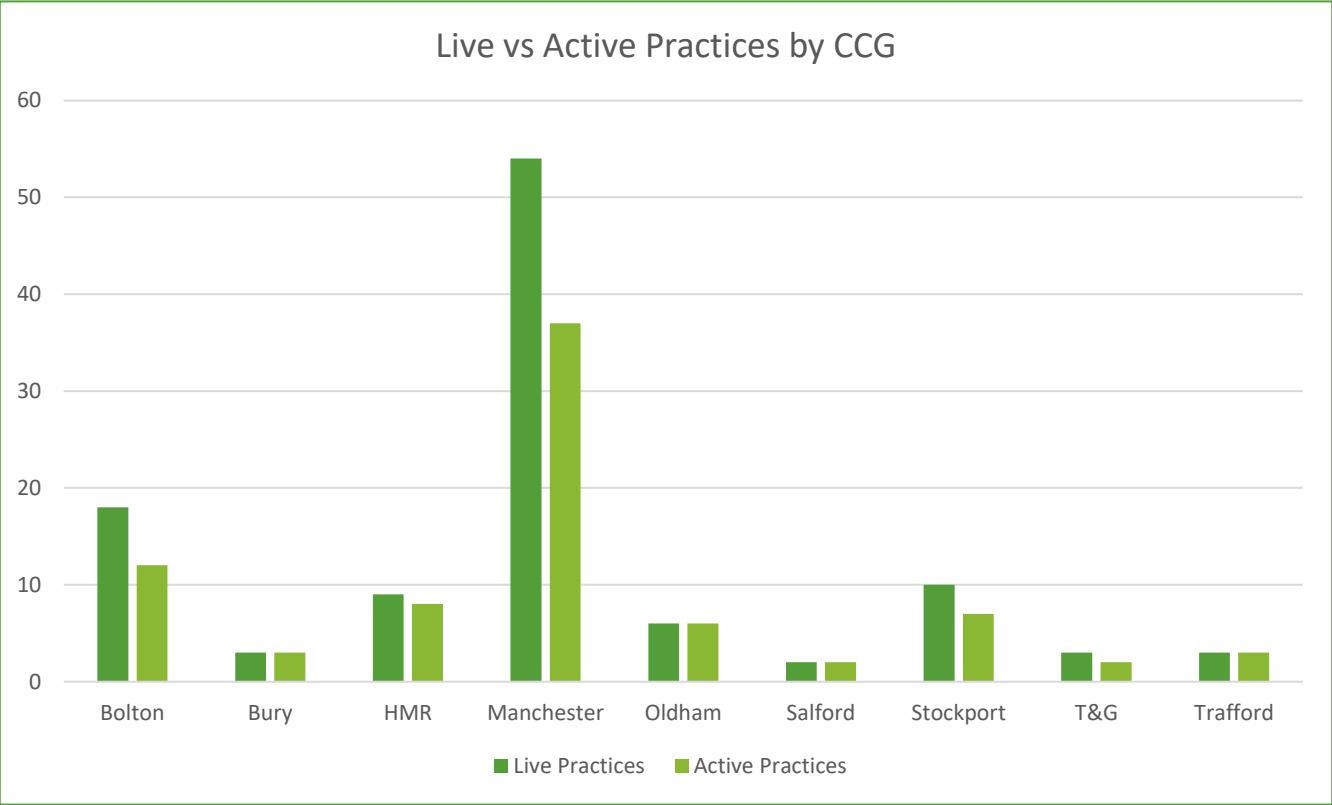

CCG	% of live practices that are active
Bolton	67%
Bury	100%
HMR	89%
Manchester	69%
Oldham	100%
Salford	100%
Stockport	70%
T&G	67%
Trafford	100%

**Practices Live : 108 (80 active – 74%)**



# Active Practices vs. PCN IIF referral targets

CCG	No. practices who met IIF target for November referrals	No. practices who did not meet IIF target for November referrals	% Active practices who met IIF target
Bolton	7	11	39%
Bury		3	0%
HMR	2	7	22%
Manchester	16	38	30%
Oldham	3	3	50%
Salford		2	0%
Stockport	4	6	40%
T&G		3	0%
Trafford	1	2	33%
Wigan			N/A

## PCN IIF Targets:

From 1<sup>st</sup> April 2022, practices are required to refer 0.65 patients per 1000 list size per week OR 34 patients per 1000 list size per year  
To qualify for the IIF incentive.

Of the 80 active practices, 33 hit their referral target in November.

# GP CPCS Objectives: Key

Objectives 1 & 2	
	On track or achieved
	Requires improvement
	Significant issues
	Not applicable

Objective #3	
Within the calendar month:	
>=75% of live practices met referral target	
>=75% of live practices made some referrals	
>25% of live practices did not make any referrals	

Objective #4	
Within the calendar month:	
>70% referrals completed within 12 hours	
60-69% referrals completed within 12 hours	
<60% referrals completed within 12 hours	

# GP CPCS Objectives: November

<b>Objectives</b>	<b>May-21</b>	<b>Jun-21</b>	<b>Jul-21</b>	<b>Aug-21</b>	<b>Sep-21</b>	<b>Oct-21</b>	<b>Nov-21</b>
<b>50% Practices live by 31/03/2022</b>	0.2%	0.2%	0.2%	0.2%	20%	23%	25%
<b>75% Practices live by 31/03/2023</b>	N/A	N/A	N/A	N/A	N/A	N/A	N/A
<b>Target number of referrals per week for live practices</b>	67%	75%	90%	89%	54%	74%	74%
<b>70% referrals completed within 12 hours</b>	96%	93%	95%	92%	84%	82%	75%

# Deployment Success Criteria: November

Success Criteria	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21
GM Processes defined, documented & signed off ready for adoption in deployment							
100% of EMIS General Practices included in the deployment plan have the EMIS CPCS template installed & ready for use by agreed date					100%	97%	100%
100% of non-EMIS General Practices included in the deployment plan have access to PharmRefer by agreed date					100%	100%	100%
95% of pharmacies identified as likely to receive referrals from a general practice included in the deployment plan have been informed & confirmed readiness	87%		100%		100%	100%	100%
80% of general practices included in the deployment plan make a referral in the week they go live	67%		100%		70%	50%	55%
70% of referrals completed by community pharmacy within timeframes specified in the service specification and toolkit – within 12 hours or the next working day.	96%	93%	95%	92%	84%	82%	75%

# Activity report



# October Referral Activity

## Consultation Outcomes:

Number of Referrals sent	Number of General Practices actively referring	Number of Pharmacies referred to
1884	80	243

Advice only  
582 (43%)

Advice & OTC sale  
304 (23%)

Advice & MAS supply  
93 (7%)

Advice & non-urgent referral  
209 (15%)

Urgent Escalation  
119 (9%)

Urgent Escalation (A&E)  
11 (0.8%)

### Escalations

Of **209 Non-urgent escalations**, 191 were to GP and 18 to other healthcare professionals.


In the pilot, it was observed that there was a greater number of non-urgent escalations in the early days of the referral pathway commencing, whilst the practice staff got used to identifying appropriate patients to refer.

It is anticipated this should average out at around 10-12% once the service is embedded.

Of **119 urgent escalations**, all were a same-day appointment request to GP.


Of **11 urgent escalations**, 4 patients were referred to A&E, 2 to the NHS 111 clinical hub and 5 to an urgent NHS walk-in

# Age of referred patients

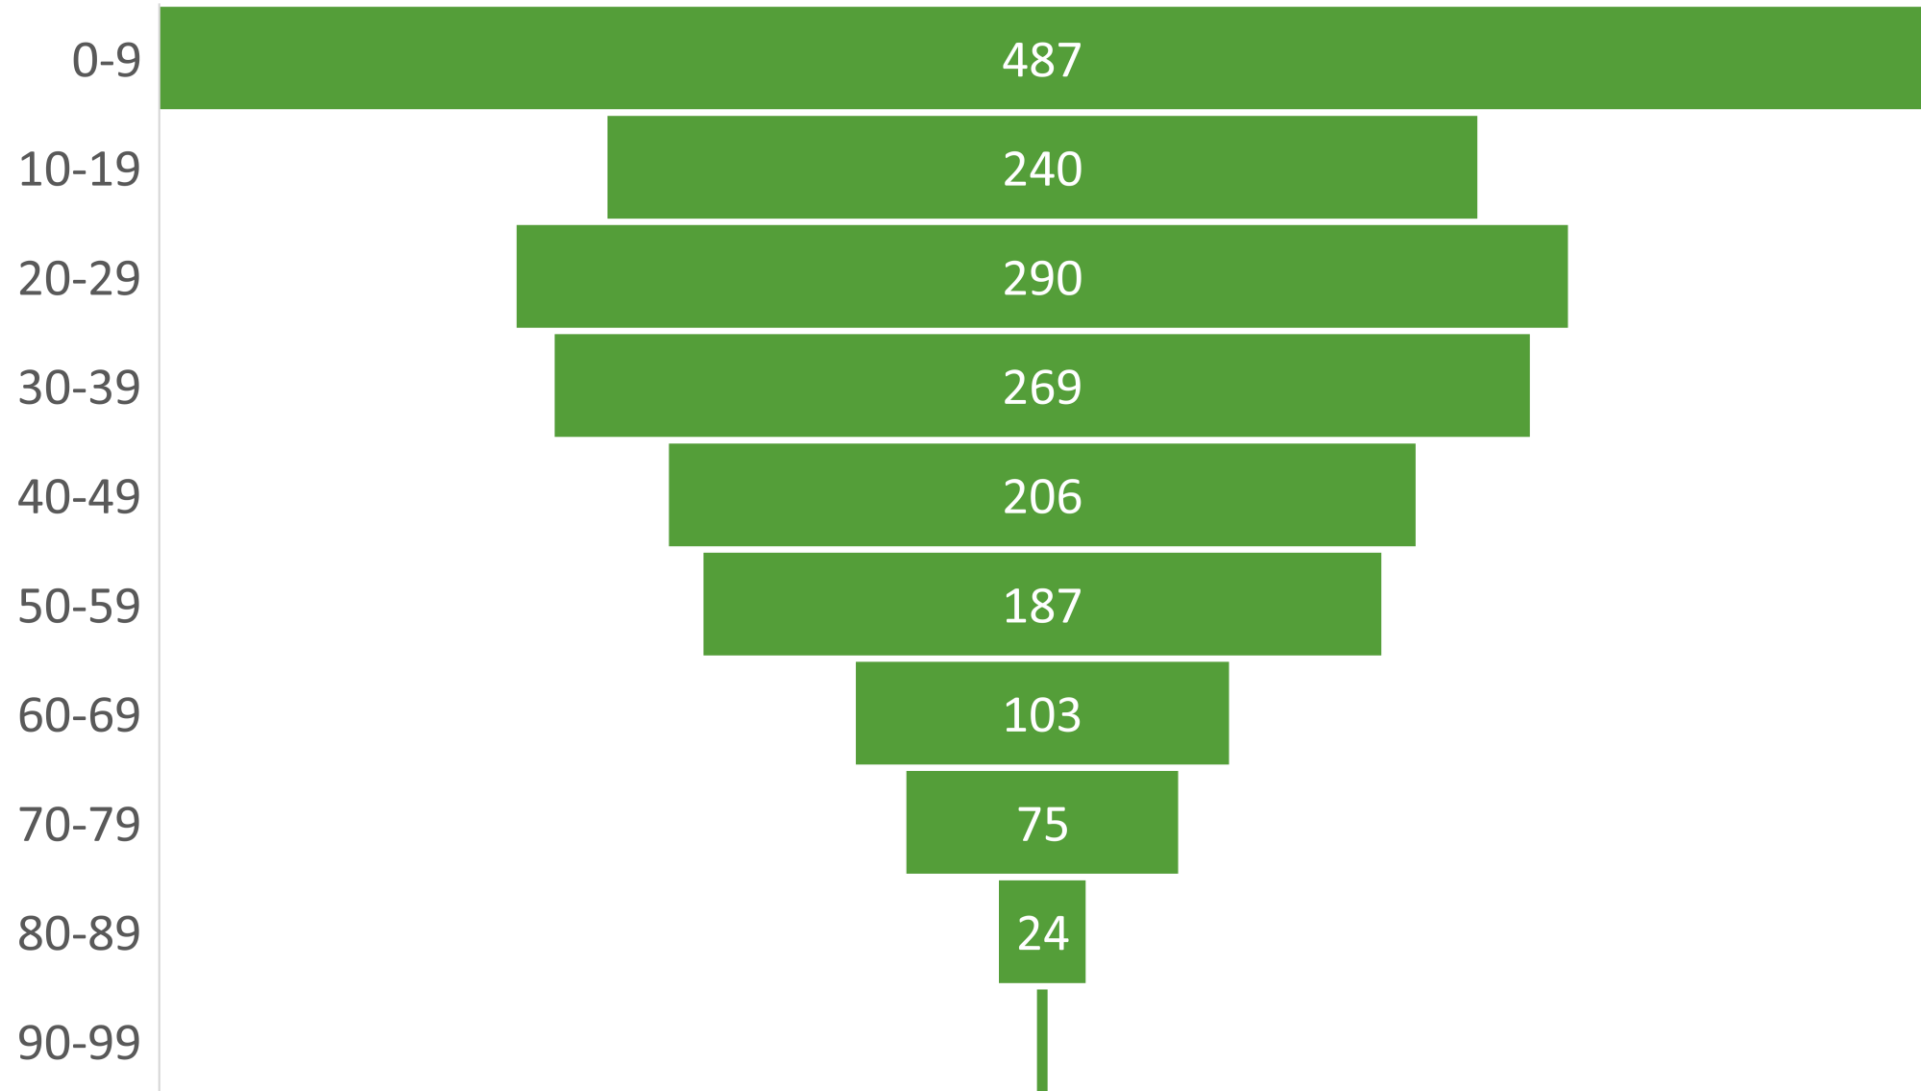



# Presenting Complaint

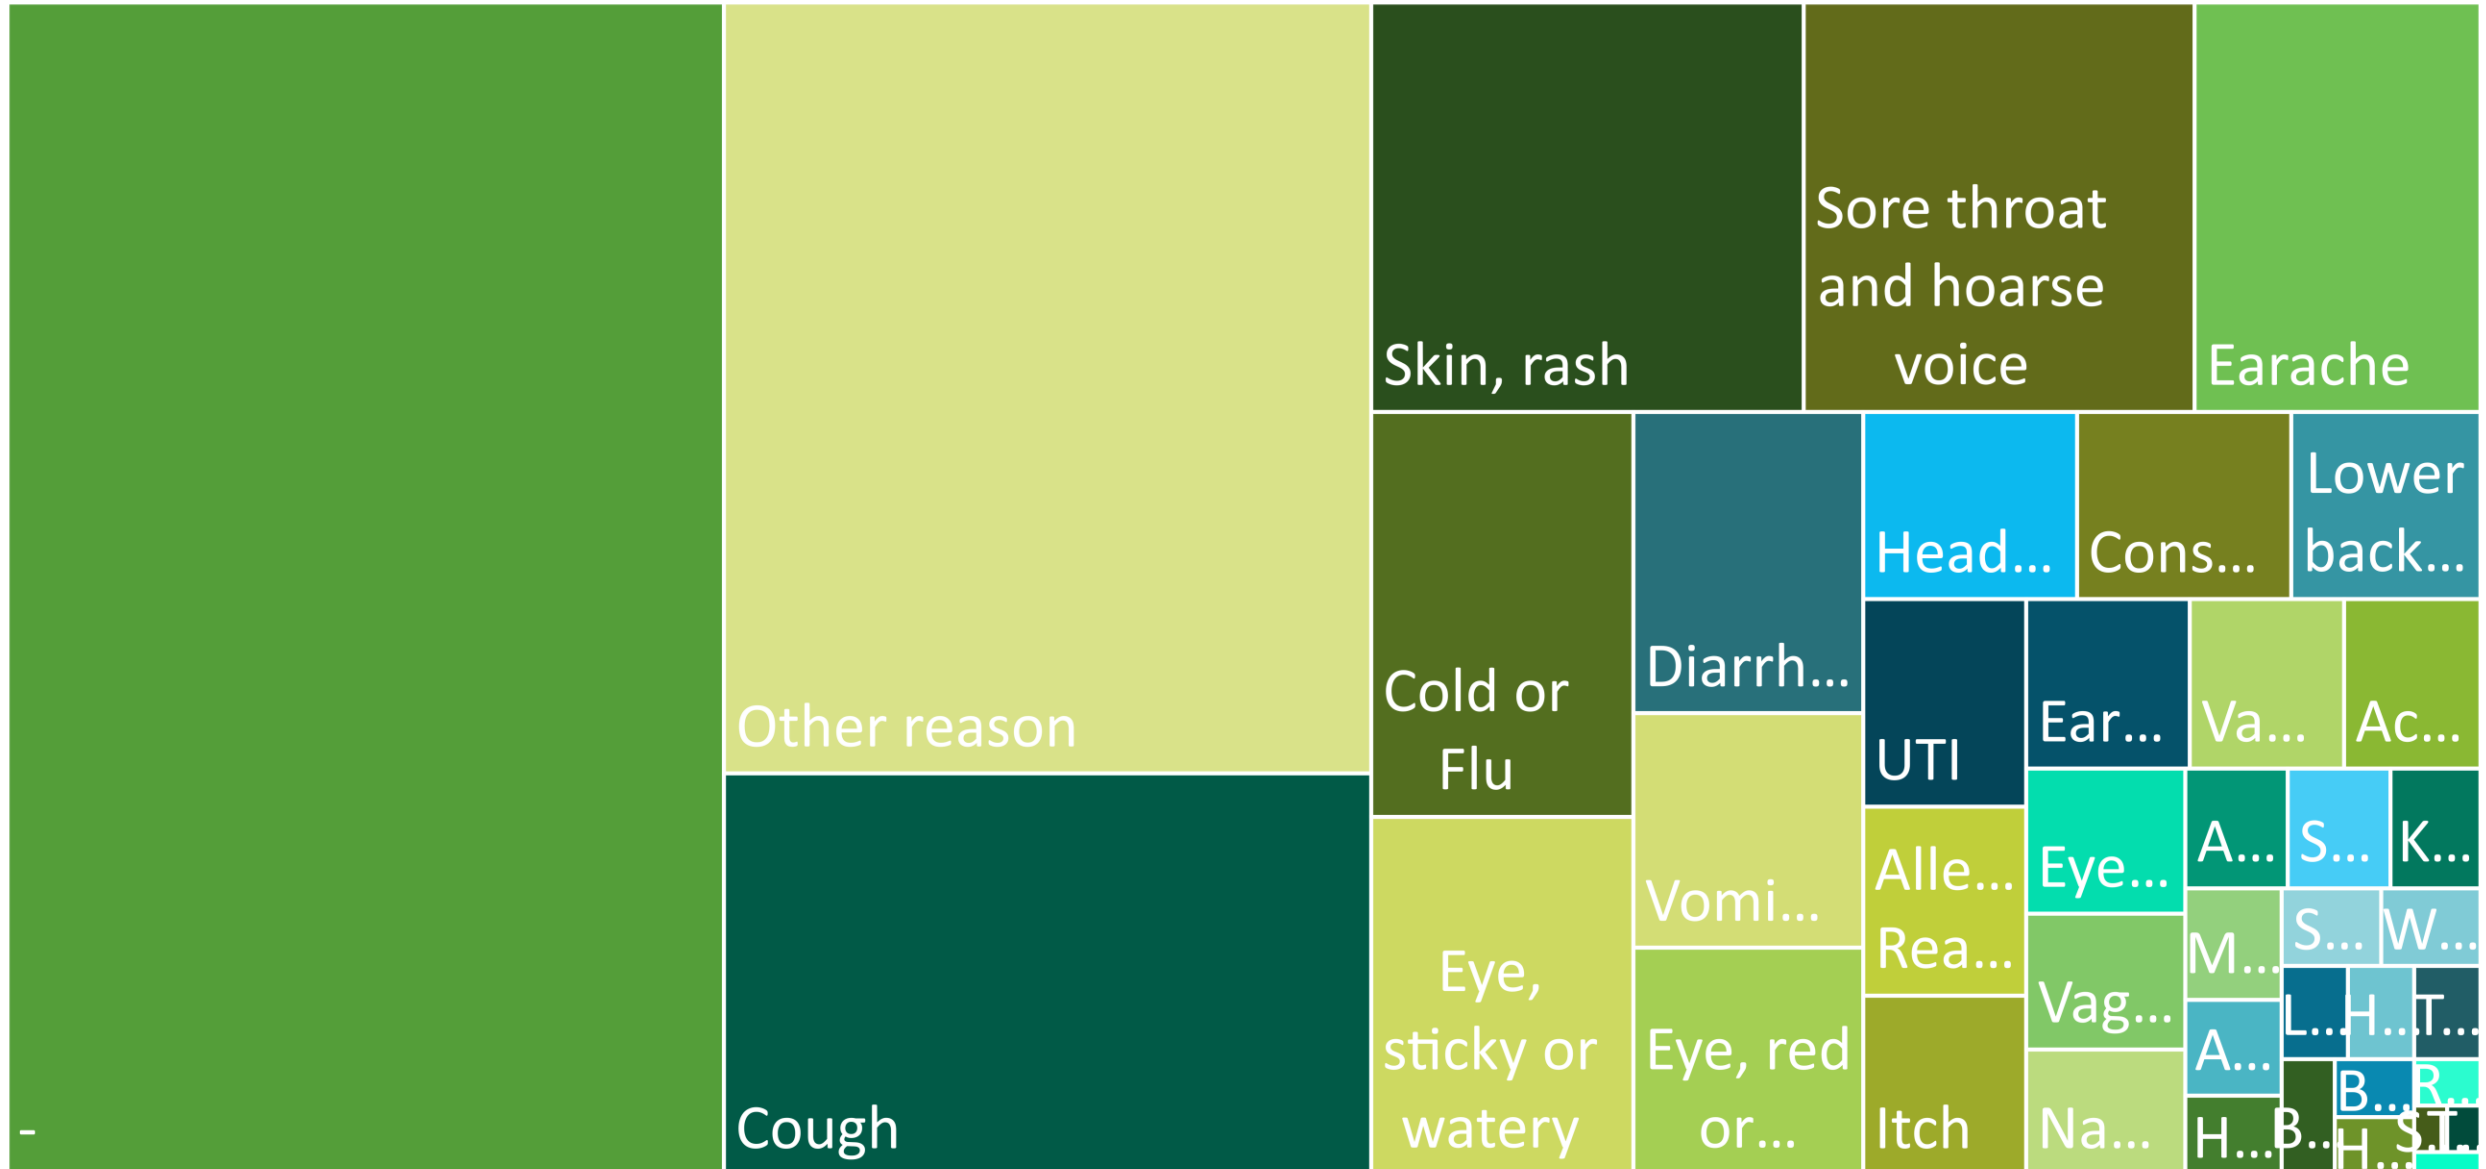

Looking ahead to next month

# Activities Planned for December:

Governance	Project Management	Engagement	Deployment
<ul style="list-style-type: none"><li>• c/f Liaise with general practice colleagues re practices live but not referring</li><li>• EMIS SBS contract received, reviewed and signed with ways of working into 2022 agreed</li><li>• Finalise PMO support and SLA arrangements for funding flow</li></ul>	<ul style="list-style-type: none"><li>• c/f Plan activity reporting to all PCNs with GMHSCP</li><li>• Support follow up of practices not completed MS form</li><li>• Prepare comms to practices to mitigate risks of go live without going through deployment</li><li>• Working group to review &amp; sign off updated blueprint &amp; associated resources</li><li>• Map pharmacies for all practices added to deployment plan following IIF/WPAF comms</li></ul>	<ul style="list-style-type: none"><li>• c/f GM association of LMCs</li><li>• Commence planning &amp; preparation for community pharmacy webinar</li></ul>	<ul style="list-style-type: none"><li>• c/f Support set-up of PharmOutcomes / Outcomes 4 Health logins for live practices re access to data and reporting &amp; then confirm to practices how to access</li><li>• Prioritise 79 practices to get go live dates agreed who have EMIS switched on</li><li>• Final decision re EMIS/PharmRefer switch on for all practices from January</li></ul>

# GM Locality Deployment Detail

# Bolton: [louise@boltonlpc.org.uk](mailto:louise@boltonlpc.org.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN
P82030	Deane Medical Centre	3 Deployment stage Implementation	BL3 5AH	Bolton	Bolton Central
P82633	Great Lever One Surgery	5 Deployment stage Post Go Live	BL3 6RN	Bolton	Bolton Central
P82036	Dr Subramanian	5 Deployment stage Post Go Live	BL3 1JF	Bolton	Brightmet & Little Lever
P82020	Dr C Hallikeri	3 Deployment stage Implementation	BL3 1JF	Bolton	Brightmet & Little Lever
P82011	Dr J Lowe & Partners (Tonge Fold)	5 Deployment stage Post Go Live	BL2 6DY	Bolton	Brightmet & Little Lever
p82001	The Dunstan Partnership	6 Implementation Completed	BL2 6NT	Bolton	Brightmet & Little Lever
P82018	Dr A Ariff & Partners (Alastair Ross)	6 Implementation Completed	BL2 6NT	Bolton	Brightmet & Little Lever
P82010	Dalefield Surgery	6 Implementation Completed	BL1 4JP	Bolton	Chorley Roads Network
P82014	Spring House	6 Implementation Completed	BL1 6AF	Bolton	Chorley Roads Network
P82031	Heaton Medical Centre	6 Implementation Completed	BL1 5PU	Bolton	Chorley Roads Network
P82627	Cornerstone surgery	5 Deployment stage Post Go Live	BL1 6AH	Bolton	Chorley Roads Network
P82634	Dr James-Authe & Partner (Wyresdale Surgery)	6 Implementation Completed	BL1 4DN	Bolton	Chorley Roads Network
P82007	Kearsley Medical Centre	6 Implementation Completed	BL4 8EP	Bolton	Farnworth & Kearsley
p82008	Stonehill Medical Centre	6 Implementation Completed	BL4 9QZ	Bolton	Farnworth & Kearsley
Y03079	Bolton Community Practice	6 Implementation Completed	BL1 8TU	Bolton	Horwich Network
P82022	Dr C Hendy & Partner	5 Deployment stage Post Go Live	BL1 3RG	Bolton	HWL Network
P82012	Dr Earnshaw & Partners (Lever Chambers 1)	3 Deployment stage Implementation	BL1 1SQ	Bolton	HWL Network
P82029	Dr M Jeyam & Partner	6 Implementation Completed	BL1 3RG	Bolton	HWL Network
P82626	Dr Uddin & Partners	6 Implementation Completed	BL1 3RG	Bolton	HWL Network
P82002	Dr Mirza (Pikes Lane 1)	3 Deployment stage Implementation	BL3 5HP	Bolton	Rumworth
P82009	Garnet Fold Practice	6 Implementation Completed	BL3 3RR	Bolton	Rumworth
P82004	Swan Lane	6 Implementation Completed	BL3 6TL	Bolton	Rumworth
P82016	Harwood Medical Centre	3 Deployment stage Implementation	BL2 3HQ	Bolton	Turton
P82643	Dr S N Liversedge & Partners	2 Deployment stage Pre-implementation	BL7 9RG	Bolton	Turton
P82006	Dr S M Malhotra & Partners	3 Deployment stage Implementation	BL6 7AN	Bolton	Horwich Network
P82025	Burnside Surgery	3 Deployment stage Implementation	BL1 8TT	Bolton	HWL Network
p82033	Dr A E Zarrouk & Partner	3 Deployment stage Implementation	BL2 1HT	Bolton	Bolton Central

Bury: [alison@cpgmhealthcare.co.uk](mailto:alison@cpgmhealthcare.co.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN	Clinical system
P83015	Ribblesdale Medical Practices	6 Implementation Completed	BL9 0SN	Bury	Bury	Vision Aeros
P83612	Mile Lane Health Centre	1 Deployment stage Initial Engagement	BL8 2JR	Bury	Horizon	Vision Aeros
P83012	Tower Family Healthcare	2 Deployment stage Pre-implementation	BL8 4AD	Bury	Horizon	Vision Aeros
P83017	Woodbank MC	2 Deployment stage Pre-implementation	BL8 1EG	Bury	Horizon	Vision Aeros
P83603	Redbank Health Centre	6 Implementation Completed	M26 2SP	Bury	Horizon	Vision Aeros
P83009	Blackford House Medical Centre	3 Deployment stage Implementation	BL9 8QA	Bury	Whitefield District & Community	Vision Aeros
P83605	Whittaker Lane Medical Centre	3 Deployment stage Implementation	M25 1EX	Bury	Prestwich	Vision Aeros
P83004	Uplands Medical Centre	3 Deployment stage Implementation	M45 8GH	Bury	Whitefield District & Community	Vision Aeros
P83011	Unsworth Medical Centre	5 Deployment stage Post Go Live	BL9 8JR	Bury	Whitefield District & Community	Vision Aeros
P83608	The Elms Medical Centre	2 Deployment stage Pre-implementation	M45 7FD	Bury	Whitefield District & Community	Vision Aeros
p83609	The Birches	3 Deployment stage Implementation	M25 2GN	Bury	Prestwich	Vision Aeros
p83007	Radcliffe Medical Practice	3 Deployment stage Implementation	M26 2SP	Bury	Bury	Vision Aeros
P83024	Knowsley Street Medical Centre	3 Deployment stage Implementation	BL9 0ST	Bury	Bury	Vision Aeros
P83010	Monarch Medical Centre	3 Deployment stage Implementation	M26 2QZ	Bury	Bury	Vision Aeros
P83620	Garden City Medical Centre	3 Deployment stage Implementation	BL0 9TN	Bury	Bury	Vision Aeros
P83025	St Gabriels Medical Centre	3 Deployment stage Implementation	M25 0HT	Bury	Prestwich	Vision Aeros
P83006	Ramsbottom HC	3 Deployment stage Implementation	BL0 9DD	Bury	Bury	Vision Aeros
P83001	Fairfax Group Practice (Prestwich HC)	3 Deployment stage Implementation	M25 1BT	Bury	Prestwich	Vision Aeros

# HMR: rikki.smeeton@gmlpc.org.uk

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN	Clinical system
P86007	Dr Caldwell & Partners	6 Implementation Completed	OL11 1AD	HMR	Canalside Health & Wellbeing Network	EMIS Web
P86009	Dr Bodner & Partners	6 Implementation Completed	OL11 3HY	HMR	Canalside Health & Wellbeing Network	EMIS Web
Y02720	The Kingsway Practice	6 Implementation Completed	OL16 4AT	HMR	Canalside Health & Wellbeing Network	EMIS Web
Y02721	Kirkholt Medical Practice	6 Implementation Completed	OL11 2JG	HMR	Canalside Health & Wellbeing Network	EMIS Web
P86011	Longford Street Group Practice	6 Implementation Completed	OL10 4NH	HMR	Heywood	EMIS Web
P86016	Heywood Health	6 Implementation Completed	OL10 3SD	HMR	Heywood	EMIS Web
P86023	Dr Osborne & Partner	6 Implementation Completed	OL10 2BS	HMR	Heywood	EMIS Web
P86602	Heady Hill Surgery	6 Implementation Completed	OL10 4RG	HMR	Heywood	EMIS Web
Y02718	Birtle View Medical Practice	6 Implementation Completed	OL10 4PW	HMR	Heywood	EMIS Web
P86021	Pennine Surgery	3 Deployment stage Implementation	OL15 8HF	HMR	Pennines	EMIS Web
P86002	Vicar's Drive Surgery (Dr Bhima)	1 Deployment stage Initial Engagement	OL11 1DN	HMR	The Bridge	EMIS Web
P86014	Dr Babar & Partners	1 Deployment stage Initial Engagement	OL16 2UP	HMR	The Bridge	EMIS Web
P86606	Dr Swamy & Partner	3 Deployment stage Implementation	OL11 2JG	HMR	The Bridge	EMIS Web
P86609	The Dale Medical Practice	1 Deployment stage Initial Engagement	OL11 1DN	HMR	The Bridge	EMIS Web
P86614	Dr Hamid	1 Deployment stage Initial Engagement	OL11 1DN	HMR	The Bridge	EMIS Web
P86619	Dr Ghafoor & Partner	2 Deployment stage Pre-implementation	OL11 1DN	HMR	The Bridge	EMIS Web

# Manchester p1:[luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN
P84005	The Vallance Centre	6 Implementation Completed	M13 9UJ	Manchester	Ardwick & Longsight
P84009	Ailsa Craig Medical Group	6 Implementation Completed	M13 0YL	Manchester	Ardwick & Longsight
P84023	Surrey Lodge Group Practice	6 Implementation Completed	M14 5BY	Manchester	Ardwick & Longsight
P84026	Dickenson Road Medical Centre	6 Implementation Completed	M13 0WQ	Manchester	Ardwick & Longsight
P84037	The Ardwick Medical Practice - prev Dr Cunningham	6 Implementation Completed	M13 9UJ	Manchester	Ardwick & Longsight
P84611	Drs Chiu, Koh & Gan	6 Implementation Completed	M13 9UJ	Manchester	Ardwick & Longsight
P84626	Wilmslow Road Medical Centre	6 Implementation Completed	M14 5LQ	Manchester	Ardwick & Longsight
P84644	Parkside Surgery	6 Implementation Completed	M12 5RU	Manchester	Ardwick & Longsight
P84689	Longsight Medical Practice	6 Implementation Completed	M13 0RR	Manchester	Ardwick & Longsight
P84030	Collegiate Medical Centre	3 Deployment stage Implementation	M8 0DA	Manchester	Cheetham Hill & Crumpsall
P84046	Cheetham Hill Primary Care Centre	2 Deployment stage Pre-implementation	M8 8AU	Manchester	Cheetham Hill & Crumpsall
P84074	Wellfield Medical Centre	2 Deployment stage Pre-implementation	M8 9JT	Manchester	Cheetham Hill & Crumpsall
P84640	Queens Medical Centre	2 Deployment stage Pre-implementation	M8 8UP	Manchester	Cheetham Hill & Crumpsall
P84645	Park View Medical Centre	2 Deployment stage Pre-implementation	M8 4RF	Manchester	Cheetham Hill & Crumpsall
P84663	The Neville Family Medical Centre	2 Deployment stage Pre-implementation	M9 8DX	Manchester	Cheetham Hill & Crumpsall
P84684	Jolly Medical Centre	3 Deployment stage Implementation	M8 9NT	Manchester	Cheetham Hill & Crumpsall
P84064	New Islington Medical Practice	6 Implementation Completed	M4 6EE	Manchester	City Centre & Ancoats
P84673	Urban Village Medical Practice	3 Deployment stage Implementation	M4 6EE	Manchester	City Centre & Ancoats
Y02849	City Health Centre	6 Implementation Completed	M1 1PL	Manchester	City Centre & Ancoats
P84042	Florence House Medical Practice	6 Implementation Completed	M11 1JG	Manchester	Clayton Beswick & Openshaw
P84041	Cornerstones Family Practice	5 Deployment stage Post Go Live	M11 3AA	Manchester	Clayton Beswick & Openshaw
P84051	Eastlands Medical Practice, Clayton Health Centre	5 Deployment stage Post Go Live	M11 4EJ	Manchester	Clayton Beswick & Openshaw
P84059	Lime Square Medical Centre	5 Deployment stage Post Go Live	M11 1DA	Manchester	Clayton Beswick & Openshaw
P84004	Five Oaks Family Practice	6 Implementation Completed	M11 3BB	Manchester	Clayton Beswick & Openshaw
P84032	Clayton Health Centre	6 Implementation Completed	M11 4EJ	Manchester	Clayton Beswick & Openshaw
P84637	Clayton Health Centre	5 Deployment stage Post Go Live	M11 4EJ	Manchester	Clayton Beswick & Openshaw
P84034	Barlow Medical Centre	6 Implementation Completed	M20 2RN	Manchester	Didsbury Chorlton Park & Burnage
P84066	David Medical Centre	5 Deployment stage Post Go Live	M21 8AH	Manchester	Didsbury Chorlton Park & Burnage
P84022	Kingsway Medical Practice	5 Deployment stage Post Go Live	M19 1UG	Manchester	Didsbury Chorlton Park & Burnage
p84678	Didsbury Medical Centre	6 Implementation Completed	M20 6BA	Manchester	Didsbury Chorlton Park & Burnage
P84016	Levenshulme Health Centre	6 Implementation Completed	M19 3BX	Manchester	Gorton & Levenshulme
P84027	West Point Medical Centre	6 Implementation Completed	M19 2AF	Manchester	Gorton & Levenshulme
P84028	Gorton Medical Centre	3 Deployment stage Implementation	M18 8LJ	Manchester	Gorton & Levenshulme
P84050	Mount Road Surgery	5 Deployment stage Post Go Live	M18 7BQ	Manchester	Gorton & Levenshulme
P84052	West Gorton Medical Practice	5 Deployment stage Post Go Live	M12 5JE	Manchester	Gorton & Levenshulme
P84053	Ashcroft Surgery	5 Deployment stage Post Go Live	M19 3BS	Manchester	Gorton & Levenshulme
Y02890	The Hawthorn Medical Centre	5 Deployment stage Post Go Live	M14 6FS	Manchester	Gorton And Levenshulme



# Manchester p2: [luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

P84605	Fernclough Surgery	2 Deployment stage Pre-implementation	M9 5RD	Manchester	H-Blackley Harpurhey & Charlestown
P84679	Willowbank Surgery	2 Deployment stage Pre-implementation	M9 4WH	Manchester	H-Blackley Harpurhey & Charlestown
P84065	The Harpurhey Health Centre	3 Deployment stage Implementation	M9 4BE	Manchester	H-Blackley Harpurhey & Charlestown
P84049	Avenue Medical Centre	3 Deployment stage Implementation	M9 6BA	Manchester	H-Blackley Harpurhey & Charlestown
P84616	Manchester Medical	6 Implementation Completed	M14 4GP	Manchester	Hulme Moss Side Rusholme & City Centre South
P84669	Cornbrook Medical Practice	6 Implementation Completed	M15 4EA	Manchester	Hulme Moss Side Rusholme & City Centre South
P84630	The Arch MP Hulme Medical Centre	6 Implementation Completed	M15 5TJ	Manchester	Hulme Moss Side Rusholme & City Centre South
P84683	The Docs	6 Implementation Completed	M1 3LY	Manchester	Hulme Moss Side Rusholme & City Centre South
P84025	St Georges Medical Centre	6 Implementation Completed	M40 5HP	Manchester	Miles Platting, Newton Heath & Moston
P84047	Droylsden Road Family Practice	3 Deployment stage Implementation	M40 1NT	Manchester	Miles Platting, Newton Heath & Moston
P84054	Whitley Road Medical Centre	6 Implementation Completed	M40 7QH	Manchester	Miles Platting, Newton Heath & Moston
P84067	Hazeldene Medical Centre	3 Deployment stage Implementation	M40 3HD	Manchester	Miles Platting, Newton Heath & Moston
P84070	Newton Heath Health Centre	3 Deployment stage Implementation	M40 2JF	Manchester	Miles Platting, Newton Heath & Moston
Y01695	Victoria Mill Medical Practice	6 Implementation Completed	M40 7LJ	Manchester	Miles Platting, Newton Heath & Moston
Y02520	Simpson Medical Practice	3 Deployment stage Implementation	M40 9NB	Manchester	Miles Platting, Newton Heath & Moston
P84012	Northenden Group Practice	5 Deployment stage Post Go Live	M22 4DH	Manchester	Northenden & Brooklands (Wythenshawe)
P84651	Northern Moor Medical Centre	6 Implementation Completed	M23 0PH	Manchester	Northenden & Brooklands (Wythenshawe)
P84045	Park Medical Centre	5 Deployment stage Post Go Live	M23 9AB	Manchester	Northenden & Brooklands (Wythenshawe)
P84672	Woodlands Medical Practice	5 Deployment stage Post Go Live	M23 9RL	Manchester	Northenden & Brooklands (Wythenshawe)
P84061	Brooklands Medical Practice	5 Deployment stage Post Go Live	M23 9JH	Manchester	Northenden & Brooklands (Wythenshawe)
P84072	The Robert Darbshire Practice Ltd.	6 Implementation Completed	M14 5NP	Manchester	Robert Darbshire Practice
P84635	The Whitswood Practice	6 Implementation Completed	M16 7AP	Manchester	Robert Darbshire Practice
Y02960	New Bank Health Centre	6 Implementation Completed	M12 4EY	Manchester	Robert Darbshire Practice

# Manchester p3: [luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

P84068	Chorlton Family Practice	5 Deployment stage Post Go Live	M21 1NJ	Manchester	West Central Manchester
P84652	Corkland Road Medical Practice	5 Deployment stage Post Go Live	M21 8UP	Manchester	West Central Manchester
P84038	Ashville Surgery	6 Implementation Completed	M16 9RT	Manchester	West Central Manchester
P84071	Wilbraham Surgery	6 Implementation Completed	M21 0UF	Manchester	West Central Manchester
P84039	The Range Medical Centre	3 Deployment stage Implementation	M16 8EE	Manchester	West Central Manchester
P84056	Princess Road Surgery	3 Deployment stage Implementation	M20 1BH	Manchester	West Central Manchester
P84650	The Alexandra Practice	2 Deployment stage Pre-implementation	M16 8NG	Manchester	West Central Manchester
P84035	Bodey Medical Centre	5 Deployment stage Post Go Live	M14 6WP	Manchester	Withington & Fallowfield
P84639	Fallowfield Medical Practice	5 Deployment stage Post Go Live	M14 6YL	Manchester	Withington & Fallowfield
P84665	Al-Shifa Medical Centre	6 Implementation Completed	M20 3HE	Manchester	Withington & Fallowfield
P84010	Borchardt Medical Centre	3 Deployment stage Implementation	M20 1EB	Manchester	Withington & Fallowfield
P84017	Ladybarn Group Practice	3 Deployment stage Implementation	M20 4SS	Manchester	Withington & Fallowfield
P84018	Mauldeth Medical Centre	3 Deployment stage Implementation	M14 6SQ	Manchester	Withington & Fallowfield
P84020	Peel Hall Medical Practice	5 Deployment stage Post Go Live	M22 5RX	Manchester	Wythenshawe
P84021	The Maples Medical Centre	6 Implementation Completed	M23 2SY	Manchester	Wythenshawe
P84024	Bowland Medical Practice	6 Implementation Completed	M23 1JX	Manchester	Wythenshawe
P84029	Benchill Medical Practice	5 Deployment stage Post Go Live	M22 9UH	Manchester	Wythenshawe
P84043	Cornishway Group Practice	3 Deployment stage Implementation	M22 5RX	Manchester	Wythenshawe
P84048	Tregenna Group Practice	3 Deployment stage Implementation	M22 0EP	Manchester	Wythenshawe
P84014	RK Medical Practice	3 Deployment stage Implementation	M22 9UH	Manchester	Wythenshawe
p84019	Valentine Medical Centre	3 Deployment stage Implementation	M9 8PP	Manchester	H-Blackley Harpurhey & Charlestown

Oldham: [alison@cpgmhealthcare.co.uk](mailto:alison@cpgmhealthcare.co.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN
p85010	Wilkinson Practice	6 Implementation Completed	OL9 0LH	Oldham	Milltown Alliance
P85011	CH Medical	5 Deployment stage Post Go Live	OL9 8NH	Oldham	Milltown Alliance
P85028	Block Lane Surgery	3 Deployment stage Implementation	OL9 7SG	Oldham	Milltown Alliance
P85605	Littletown Family Medical Practice	3 Deployment stage Implementation	OL8 4LR	Oldham	Milltown Alliance
P85612	Werneth Medical Practice	2 Deployment stage Pre-implementation	OL8 4AL	Oldham	Milltown Alliance
P85018	Dr Danson	6 Implementation Completed	OL9 7AY	Oldham	Milltown Alliance
P85004	Dr Akhter & Partners	3 Deployment stage Implementation	OL9 0LH	Oldham	Milltown Alliance
P85014	Hopwood House Medical Practice	5 Deployment stage Post Go Live	OL4 1JN	Oldham	Oldham Central
P85615	Kapur Family Care	6 Implementation Completed	OL9 7AY	Oldham	Milltown Alliance
P85005	Leesbrook Surgery	5 Deployment stage Post Go Live	OL4 3DG	Oldham	Oldham East
P85016	Saddleworth Medical Practice	1 Deployment stage Initial Engagement	OL3 6AH	Oldham	Oldham East
P85022	Lees Medical Practice	1 Deployment stage Initial Engagement	OL4 3BP	Oldham	Oldham East
P85606	Moorside Medical Practice	1 Deployment stage Initial Engagement	OL1 4JU	Oldham	Oldham East
P89006	Pennine Medical Centre	1 Deployment stage Initial Engagement	OL5 9AJ	Oldham	Oldham East
P85602	Saraf Medical Practice	1 Deployment stage Initial Engagement	OL1 4JU	Oldham	Oldham East
P85020	Springfield House Medical Centre	3 Deployment stage Implementation	OL4 2RJ	Oldham	Oldham East

Salford: [rikki@gmlpc.org.uk](mailto:rikki@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN
P87022	Drs Kassam & Pira	3 Deployment stage Implementation	M7 1QE	Salford	Broughton Health Alliance
P87026	Newbury Green Medical Practice	1 Deployment stage Initial Engagement	M7 4NX	Salford	Broughton Health Alliance
P87020	St Andrews MC	1 Deployment stage Initial Engagement	M30 0NU	Salford	Eccles & Irlam
P87024	Springfield Medical Centre	5 Deployment stage Post Go Live	M30 8QD	Salford	Eccles & Irlam
P87610	The Mosslands Medical Practice	4 Deployment stage Go Live	M44 5LH	Salford	Eccles & Irlam
P87620	Monton Medical Centre	1 Deployment stage Initial Engagement	M30 8AR	Salford	Eccles & Irlam
P87649	Chapel Group Medical Centre	2 Deployment stage Pre-implementation	M44 6FE	Salford	Eccles & Irlam
P87657	Salford Care Centres Irlam	3 Deployment stage Implementation	M44 6DP	Salford	Eccles & Irlam
Y00445	Salford Primary Care Together	3 Deployment stage Implementation	M7 3SE	Salford	Eccles & Irlam
P87004	Salford Medical Centre	3 Deployment stage Implementation	M6 5PP	Salford	Ordsall & Claremont
P87015	Pendleton Medical Centre	3 Deployment stage Implementation	M6 5FX	Salford	Ordsall & Claremont
P87027	Langworthy Medical Practice	3 Deployment stage Implementation	M6 5WW	Salford	Ordsall & Claremont
P87032	Orient Rd Medical Practice	3 Deployment stage Implementation	M6 8LE	Salford	Ordsall & Claremont
P87035	Ordsall Health Surgery	3 Deployment stage Implementation	M5 3PH	Salford	Ordsall & Claremont
P87040	Sorrel Group Practice	3 Deployment stage Implementation	M6 7HL	Salford	Ordsall & Claremont
P87634	Clarendon Surgery	3 Deployment stage Implementation	M6 5FX	Salford	Ordsall & Claremont
P87639	Cornerstone Medical Practice	3 Deployment stage Implementation	M6 5QQ	Salford	Ordsall & Claremont
P87658	The Willows Medical Practice	3 Deployment stage Implementation	M5 5JR	Salford	Ordsall & Claremont
Y02767	The Height General Practice	2 Deployment stage Pre-implementation	M6 7NJ	Salford	Ordsall & Claremont
p87019	Silverdale Medical Practice	1 Deployment stage Initial Engagement	M27 8HP	Salford	Swinton
P87025	Dr Stedman & Partners	2 Deployment stage Pre-implementation	M27 4AF	Salford	Swinton
P87002	Dr J Harris & Partners	1 Deployment stage Initial Engagement	M27 0NA	Salford	Swinton
P87016	Dr G K Jolly & Partners	1 Deployment stage Initial Engagement	M27 0EW	Salford	Swinton
P87008	Dr B Sutherland & Partners	3 Deployment stage Implementation	M28 3AT	Salford	Walkden & Little Hulton
P87017	The Limes Medical Centre	3 Deployment stage Implementation	M28 3AT	Salford	Walkden & Little Hulton
P87028	Dr Browne & Partners	1 Deployment stage Initial Engagement	M28 3DR	Salford	Walkden & Little Hulton
P87613	Cleggs Lane Medical Practice	3 Deployment stage Implementation	M38 9RS	Salford	Walkden & Little Hulton
P87618	Dr Y Loomba	1 Deployment stage Initial Engagement	M28 3EZ	Salford	Walkden & Little Hulton
P87624	Dr S Mccorkindale & Partners	1 Deployment stage Initial Engagement	M28 1PB	Salford	Walkden & Little Hulton
P87625	Dearden Avenue Medical Practice	3 Deployment stage Implementation	M38 9GH	Salford	Walkden & Little Hulton
P87627	Dr Nagesh Chennupati	1 Deployment stage Initial Engagement	M28 1LZ	Salford	Walkden & Little Hulton
P87630	Cherry Medical Practice	1 Deployment stage Initial Engagement	M28 0AY	Salford	Walkden & Little Hulton
P87661	Dr M T Khan	1 Deployment stage Initial Engagement	M38 9LQ	Salford	Walkden & Little Hulton
p87008	Dr B Sutherland & Partners	3 Deployment stage Implementation	M28 3AT	Salford	Walkden & Little Hulton
P87654	Dr I Jeet & Partner	2 Deployment stage Pre-implementation	M7 1RD	Salford	Broughton Health Alliance

# Stockport: [rikki@gmlpc.org.uk](mailto:rikki@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN
P88025	Dr Shipston AM & Partners	1 Deployment stage Initial Engagement	SK8 6LU	Stockport	Bramhall & Cheadle Hulme
P88020	Cheadle Medical Practice	6 Implementation Completed	SK8 1BH	Stockport	Cheadle Network
P88023	Heald Green Health Centre 2	6 Implementation Completed	SK8 3JD	Stockport	Cheadle Network
P88024	Gatley Medical Centre	6 Implementation Completed	SK8 4DG	Stockport	Cheadle Network
P88042	Heald Green Health Centre 1	6 Implementation Completed	SK8 3JD	Stockport	Cheadle Network
P88002	Dr Hedley PJ & Partners	1 Deployment stage Initial Engagement	SK6 5AA	Stockport	Hazel Grove High Lane & Marple
P88006	Heaton Norris Health Centre	1 Deployment stage Initial Engagement	SK6 6BW	Stockport	Hazel Grove High Lane & Marple
P88012	Heaton Norris Health Centre	1 Deployment stage Initial Engagement	SK7 4QR	Stockport	Hazel Grove High Lane & Marple
P88021	Dr Valluri & Partners	1 Deployment stage Initial Engagement	SK6 6AB	Stockport	Hazel Grove High Lane & Marple
P88606	Dr Aldabbagh	1 Deployment stage Initial Engagement	SK7 4AA	Stockport	Hazel Grove High Lane & Marple
P88623	Dr Mathewson RCL & Partners	1 Deployment stage Initial Engagement	SK6 8DR	Stockport	Hazel Grove High Lane & Marple
P88005	Family Surgery	6 Implementation Completed	SK5 6RN	Stockport	Tame Valley
P88011	Heaton Norris Health Centre	5 Deployment stage Post Go Live	SK4 1JX	Stockport	Tame Valley
P88018	Park View Group Practice	6 Implementation Completed	SK5 6ET	Stockport	Tame Valley
P88043	Brinnington Health Centre	6 Implementation Completed	SK5 8BS	Stockport	Tame Valley
P88610	South Reddish Medical Centre	6 Implementation Completed	SK5 7QU	Stockport	Tame Valley
P88615	Vernon Park Surgery	6 Implementation Completed	SK1 2EX	Stockport	Tame Valley
P88009	South Reddish Medical Centre	1 Deployment stage Initial Engagement	SK6 1ND	Stockport	Werneth
P88017	Dr Spreckley DE & Partners	1 Deployment stage Initial Engagement	SK6 4QR	Stockport	Werneth
P88019	Dr Gallagher J & Partner	1 Deployment stage Initial Engagement	SK6 2AH	Stockport	Werneth
P88044	Dr Armstrong MH & Partners	1 Deployment stage Initial Engagement	SK6 2AH	Stockport	Werneth
P88607	Dr Patel R & Partner	1 Deployment stage Initial Engagement	SK6 4QR	Stockport	Werneth
P88625	Archwood Medical Practice	3 Deployment stage Implementation	SK6 1ND	Stockport	Werneth

T&G: [alison@cpgmhealthcare.co.uk](mailto:alison@cpgmhealthcare.co.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN
p89020	HT PRACTICE	2 Deployment stage Pre-implementation	OL6 7SR	T&G	Ashton
P89010	Medlock Vale Medical Practice	2 Deployment stage Pre-implementation	M43 7BW	T&G	Denton
P89029	Market Street Medical Practice	1 Deployment stage Initial Engagement	M43 6DE	T&G	Denton
Y02663	Droylsden Medical Practice	2 Deployment stage Pre-implementation	M43 7NP	T&G	Denton
Y02713	Guide Bridge Medical Practice	1 Deployment stage Initial Engagement	M34 5HY	T&G	Denton
P89015	Millgate Healthcare Partnership	3 Deployment stage Implementation	M34 2AJ	T&G	Denton
P89018	Denton Medical Practice	3 Deployment stage Implementation	M34 3JE	T&G	Denton
P89002	The Brooke Surgery	2 Deployment stage Pre-implementation	SK14 1AT	T&G	Hyde
P89004	Awburn House Surgery	3 Deployment stage Implementation	SK14 6LA	T&G	Hyde
P89012	Clarendon Medical Centre	3 Deployment stage Implementation	SK14 2AQ	T&G	Hyde
P89013	Hattersley Group Practice	3 Deployment stage Implementation	SK14 3EH	T&G	Hyde
P89014	Haughton Thornley Medical Centres	1 Deployment stage Initial Engagement	SK14 1JY	T&G	Hyde
P89016	Donneybrook Medical Centre	3 Deployment stage Implementation	SK14 2AH	T&G	Hyde
P89021	Dukinfield Medical Centre	1 Deployment stage Initial Engagement	SK16 4DB	T&G	Hyde
P89602	The Smithy Surgery	2 Deployment stage Pre-implementation	SK14 8LN	T&G	Hyde
P89005	Lockside Medical Centre	6 Implementation Completed	SK15 2PT	T&G	Stalybridge
P89007	Staveleigh Medical Centre	6 Implementation Completed	SK15 2AE	T&G	Stalybridge
P89026	Grosvenor Medical Centre	3 Deployment stage Implementation	SK15 1RZ	T&G	Stalybridge
P89612	Mossley Medical Practice	2 Deployment stage Pre-implementation	OL5 9AB	T&G	Stalybridge
P89618	The Pike Medical Centre	2 Deployment stage Pre-implementation	OL5 0HE	T&G	Stalybridge
P89022	King Street Medical Centre	3 Deployment stage Implementation	SK16 4JZ	T&G	Stalybridge
P89023	St. Andrews House	3 Deployment stage Implementation	SK15 2AU	T&G	Stalybridge
Y02936	Millbrook Medical Practice	2 Deployment stage Pre-implementation	SK15 3BJ	T&G	Stalybridge
P89025	Town Hall Surgery	6 Implementation Completed	SK16 4LD	T&G	Stalybridge
c81106	Lambgates Surgery	3 Deployment stage Implementation	SK13 1DJ	T&G	Glossop
C81640	Simmondley Medical Practice	3 Deployment stage Implementation	SK13 6NN	T&G	Glossop
P89609	Stamford House Medical Centre	2 Deployment stage Pre-implementation	OL6 9QH	T&G	Ashton
P89008	Ashton Medical Group	2 Deployment stage Pre-implementation	OL6 6HD	T&G	Ashton
C81077	Howard Street Medical Practice	3 Deployment stage Implementation	SK13 7DE	T&G	Glossop
C81615	Cottage Lane Surgery	2 Deployment stage Pre-implementation	SK13 6EQ	T&G	Glossop

Trafford: [luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN
P91604	St Johns Medical Centre	3 Deployment stage Implementation	WA14 1PF	Trafford	Altrincham Healthcare Alliance
P91003	Park Medical Practice	1 Deployment stage Initial Engagement	WA15 6QQ	Trafford	Altrincham Healthcare Alliance
P91004	Altrincham Medical Practice	3 Deployment stage Implementation	WA14 2DD	Trafford	Altrincham Healthcare Alliance
P91008	Shay Lane Medical Centre	3 Deployment stage Implementation	WA15 8NZ	Trafford	Altrincham Healthcare Alliance
P91016	West Timperley Health Centre	3 Deployment stage Implementation	WA14 5PF	Trafford	Altrincham Healthcare Alliance
P91020	Brooks Bar Medical Centre	2 Deployment stage Pre-implementation	M16 9NW	Trafford	North Trafford
P91018	The Delamere Medical Practice	1 Deployment stage Initial Engagement	M32 0DF	Trafford	North Trafford
P91013	Boundary House Medical Centre	1 Deployment stage Initial Engagement	M33 2RH	Trafford	Sale Central
P91014	Washway Road Medical Centre	1 Deployment stage Initial Engagement	M33 7SS	Trafford	Sale Central
P91017	Bodmin Road Health Centre	1 Deployment stage Initial Engagement	M33 5JH	Trafford	Sale Central
P91021	Firsway Health Centre	1 Deployment stage Initial Engagement	M33 4BR	Trafford	Sale Central
P91035	Conway Road Health Centre	1 Deployment stage Initial Engagement	M33 2TB	Trafford	Sale Central
P91006	The Urmston Group Practice	6 Implementation Completed	M41 8AA	Trafford	Trafford West
P91009	Davyhulme Medical Centre	6 Implementation Completed	M41 7WJ	Trafford	Trafford West
P91012	Primrose Surgery	6 Implementation Completed	M41 7AB	Trafford	Trafford West

# Wigan: [luvjit@gmlpc.org.uk](mailto:luvjit@gmlpc.org.uk)

Practice code	Practice Name	Deployment stage	Practice post code	Locality	PCN
P92016	Pennygate Medical Centre	3 Deployment stage Implementation	WN2 2QG	Wigan	Hindley
P92620	SSP Health Ltd	1 Deployment stage Initial Engagement	WN3 4NW	Wigan	Hindley
P92616	Higher Ince Surgery, Ince Community Clinic	3 Deployment stage Implementation	WN2 2DJ	Wigan	Hindley
P92006	ALEXANDER HOUSE SURGERY	3 Deployment stage Implementation	WN2 5NG	Wigan	Hindley
P92031	Platt House Surgery	2 Deployment stage Pre-implementation	WN2 5NG	Wigan	Hindley
Y02274	Rivington Way Surgery	3 Deployment stage Implementation	WN2 5NG	Wigan	Hindley
P92004	Dr Tun & Partners	3 Deployment stage Implementation	WN2 3HQ	Wigan	Hindley
P92007	Wong & Partners	1 Deployment stage Initial Engagement	WN7 2PG	Wigan	Leigh
P92023	Brookmill Medical Centre	3 Deployment stage Implementation	WN7 2RB	Wigan	Leigh
P92029	Westleigh Medical Practice	3 Deployment stage Implementation	WN2 5XB	Wigan	Leigh
P92035	Lilford Park Surgery	1 Deployment stage Initial Engagement	WN7 1HR	Wigan	Leigh
P92602	Foxleigh Family Surgery	3 Deployment stage Implementation	WN7 2PE	Wigan	Leigh
P92607	Grasmere Surgery	3 Deployment stage Implementation	WN7 1HR	Wigan	Leigh
P92615	The Avenue Surgery	3 Deployment stage Implementation	WN7 1HR	Wigan	Leigh
P92621	Premier Health	2 Deployment stage Pre-implementation	WN7 2PE	Wigan	Leigh
Y00050	Pennington Park Surgery	3 Deployment stage Implementation	WN7 2PE	Wigan	Leigh
Y02322	Leigh Family Practice	1 Deployment stage Initial Engagement	WN7 2PE	Wigan	Leigh
Y02886	Leigh Sports Village	2 Deployment stage Pre-implementation	WN7 4JY	Wigan	Leigh
P92651	The Surgery	1 Deployment stage Initial Engagement	WA3 2AQ	Wigan	LiGA Wigan
Y02378	Ashton Clinic	1 Deployment stage Initial Engagement	WN4 8LB	Wigan	LiGA Wigan
P92041	Ashton Medical Centre 120 Wigan Rd	1 Deployment stage Initial Engagement	WN4 9SU	Wigan	LiGA Wigan
P92012	Golborne Health Centre	3 Deployment stage Implementation	WA3 3GS	Wigan	LiGA Wigan
P92639	Golborne Health Centre	3 Deployment stage Implementation	WA3 3GS	Wigan	LiGA Wigan
P92630	The Golborne Surgery	3 Deployment stage Implementation	WN4 9PT	Wigan	LiGA Wigan
P92648	Slag Lane Medical Centre	3 Deployment stage Implementation	WA3 2EZ	Wigan	LiGA Wigan
P92002	The Surgery	1 Deployment stage Initial Engagement	WA3 2HY	Wigan	LiGA Wigan
P92010	Beech Hill Medical Practice	3 Deployment stage Implementation	WN6 7PD	Wigan	North Wigan
P92014	Standish Medical Practice	3 Deployment stage Implementation	WN6 0HD	Wigan	North Wigan
P92015	Aspull Surgery	3 Deployment stage Implementation	WN2 1XH	Wigan	North Wigan
P92017	Shevington Surgery	3 Deployment stage Implementation	WN6 8ET	Wigan	North Wigan
P92024	Dr Kumar (The Chandler Surgery)	3 Deployment stage Implementation	WN3 5HL	Wigan	SWAN Network Wigan
P92653	Shakespeare Surgery Ltd	3 Deployment stage Implementation	WN3 5HL	Wigan	SWAN Network Wigan
P92005	The Grange Practice	2 Deployment stage Pre-implementation	WN3 5HL	Wigan	SWAN Network Wigan
P92001	Medicentre	3 Deployment stage Implementation	WN4 9AZ	Wigan	SWAN Network Wigan
P92034	Bryn Cross Surgery	3 Deployment stage Implementation	WN4 0AR	Wigan	SWAN Network Wigan
P92647	Hawkley Brook Medical Practice	3 Deployment stage Implementation	WN3 5HL	Wigan	SWAN Network Wigan
P92038	Winstanley Medical Centre	3 Deployment stage Implementation	WN3 6JN	Wigan	SWAN Network Wigan
P92642	Marus Bridge Practice	3 Deployment stage Implementation	WN3 5HL	Wigan	SWAN Network Wigan
Y02321	Poplar Street Surgery	3 Deployment stage Implementation	M29 8AX	Wigan	TABA Wigan
P92633	Beefold Medical Centre	2 Deployment stage Pre-implementation	M46 0BD	Wigan	TABA Wigan
P92637	Astley General Practice (SSP Health)	3 Deployment stage Implementation	M29 7BY	Wigan	TABA Wigan
P92042	Dr KK Chan & partners	2 Deployment stage Pre-implementation	M46 9DE	Wigan	TABA Wigan
P92033	Dr CP Khatri & Partners	3 Deployment stage Implementation	M29 8AL	Wigan	TABA Wigan
P92646	Dr Vardhan's Surgery	2 Deployment stage Pre-implementation	M29 7HG	Wigan	TABA Wigan
P92605	Anderson & Partner	3 Deployment stage Implementation	M28 1BZ	Wigan	TABA Wigan
P92020	Sivakumar & Partner	2 Deployment stage Pre-implementation	M29 7BS	Wigan	TABA Wigan
P92003	The Dicconson Group Practice	3 Deployment stage Implementation	WN6 7LB	Wigan	Wigan Central
P92008	Bradshaw Medical Centre	3 Deployment stage Implementation	WN5 0AB	Wigan	Wigan Central
P92011	Sullivan Way Surgery	3 Deployment stage Implementation	WN1 3TB	Wigan	Wigan Central
P92019	Pemberton Surgery	3 Deployment stage Implementation	WN5 9QX	Wigan	Wigan Central
P92021	Newtown Medical Practice	2 Deployment stage Pre-implementation		0Wigan	Wigan Central
P92026	Patel, Kamath & Partners	3 Deployment stage Implementation	WN1 3NH	Wigan	Wigan Central
